

SYSTEM UTILIZATION AND RELIABILITY MONTHLY REPORT

for the month ending
August 2013

<http://www.transcanada.com/customerexpress/2885.html>

Published date:
December 03, 2013

Highlights This Month:

- The average actual flow for the dominant flow condition in each of the Alberta design areas is compared against the corresponding design capability to obtain a measure of pipeline utilization. Consequently, design capability utilization is measured as Average Actual Flow / Seasonal Design Capability.
- The Firm Transportation service contract utilization table (page 3 of this report) illustrates the FT and FT + IT utilization for receipts and deliveries.
- The Historical Transportation Service Availability Report has been removed. FT Receipt and Border Availability information is available from the NrG website:
<http://www.nrgexpressway.com/servlet/nrginfo.ew.EWLauncher?RUN=nrginfo.ew.notices.Se archNotices&tsp=NGTL&critical=A>

NOVA Gas Transmission Ltd.

TABLE OF CONTENTS

<u>MONTHLY FEATURES</u>	PAGE
Firm Transportation Service Contract Utilization	3
Design Capability Utilization	
Ft. McMurray Area – Flow Within.....	4
Kirby Area – Flow Within.....	5
North of Bens Lake – Flow Within.....	6
North & South of Bens Lake – Flow Within.....	7
Upper Peace River	8
Upper & Central Peace River	9
Peace River Design	10
Upstream James River	11
South & Alderson – Flow Within	12
Rimbey Nevis – Flow Within	13
Eastern Alberta Mainline (James River to Princess)	14
Medicine Hat - Flow Within	15
Eastern Alberta Mainline (Princess to Empress/McNeill)	16
Western Alberta Mainline (AB/BC & AB/Montana Borders)	17
Future Firm Transportation Service Availability.....	18
How to Use This Report	19
<u>REFERENCES</u>	
NGTL Design Areas Map	20
NGTL Pipeline Segments Map	21
Definition of Terms	22

If you have any questions on the content of this report, contact Winston Cao at (403) 920-5315 or via fax at (403) 920-2357.

FIRM TRANSPORTATION SERVICE¹ CONTRACT UTILIZATION³



By NGTL Pipeline Segments
August 2013

Segment	Contract	Delivery		Receipt	
		Utilization	Aug CD (TJ/d)	Utilization	Aug CD (MMcf/d)
UPRM	FT	4%	25.4	96%	70
	FT + IT ²	12%		116%	
PRL	FT	31%	42.2	93%	107
	FT + IT	31%		115%	
NWML	FT	20%	5.0	43%	706
	FT + IT	22%		46%	
GRDL	FT	9%	8.9	61%	1,669
	FT + IT	313%		66%	
WRSY	FT	0%	0.0	86%	21
	FT + IT	0%		107%	
WAEX	FT	11%	15.4	70%	287
	FT + IT	29%		88%	
JUDY	FT	21%	45.1	92%	102
	FT + IT	23%		110%	
GPML	FT	25%	164.5	86%	3,022
	FT + IT	39%		92%	
CENT	FT	6%	10.4	93%	825
	FT + IT	12%		115%	
LPOL	FT	25%	81.8	94%	531
	FT + IT	39%		129%	
WGAT	FT	67%	3,334.8	84%	419
	FT + IT	68%		100%	
ALEG	FT	31%	320.9	97%	855
	FT + IT	45%		120%	
SLAT	FT	14%	169.2	97%	223
	FT + IT	14%		117%	
MLAT	FT	52%	262.1	90%	224
	FT + IT	68%		105%	
BLEG	FT	40%	144.2	96%	588
	FT + IT	42%		109%	
EGAT	FT	95%	3,184.7	97%	38
	FT + IT	116%		116%	
MRTN	FT	10%	38.8	89%	77
	FT + IT	16%		108%	
LIEG	FT	77%	1,153.4	59%	29
	FT + IT	89%		172%	
KIRB	FT	66%	1,082.3	75%	38
	FT + IT	67%		135%	
SMHI	FT	40%	12.0	80%	38
	FT + IT	40%		132%	
REDL	FT	8%	13.1	64%	44
	FT + IT	11%		119%	
COLD	FT	42%	85.7	68%	37
	FT + IT	85%		86%	
EDM	FT	36%	1,692.5	98%	61
	FT + IT	37%		132%	
NLAT	FT	12%	15.4	98%	138
	FT + IT	12%		136%	
WAIN	FT	4%	0.4	79%	8
	FT + IT	4%		163%	
ELAT	FT	75%	258.2	90%	132
	FT + IT	78%		130%	
TOTAL SYSTEM	FT	67%	12,166.7	82%	10,288
	FT + IT	75%		96%	

***NOTE:**



1. FT includes all receipt and delivery Firm Transportation Services: FTR, FTRN, LRS, FID1, FID2,
2. IT includes all receipt and delivery Interruptible Services: ITR, FRO, IID1, IID2, and FDO.
3. Utilization data is based on billed monthly volumes. Percent utilization calculated as FT and FT + IT billed volumes divided by applicable receipt or delivery Contract level.

DESIGN CAPABILITY UTILIZATION FT. McMURRAY AREA – FLOW WITHIN

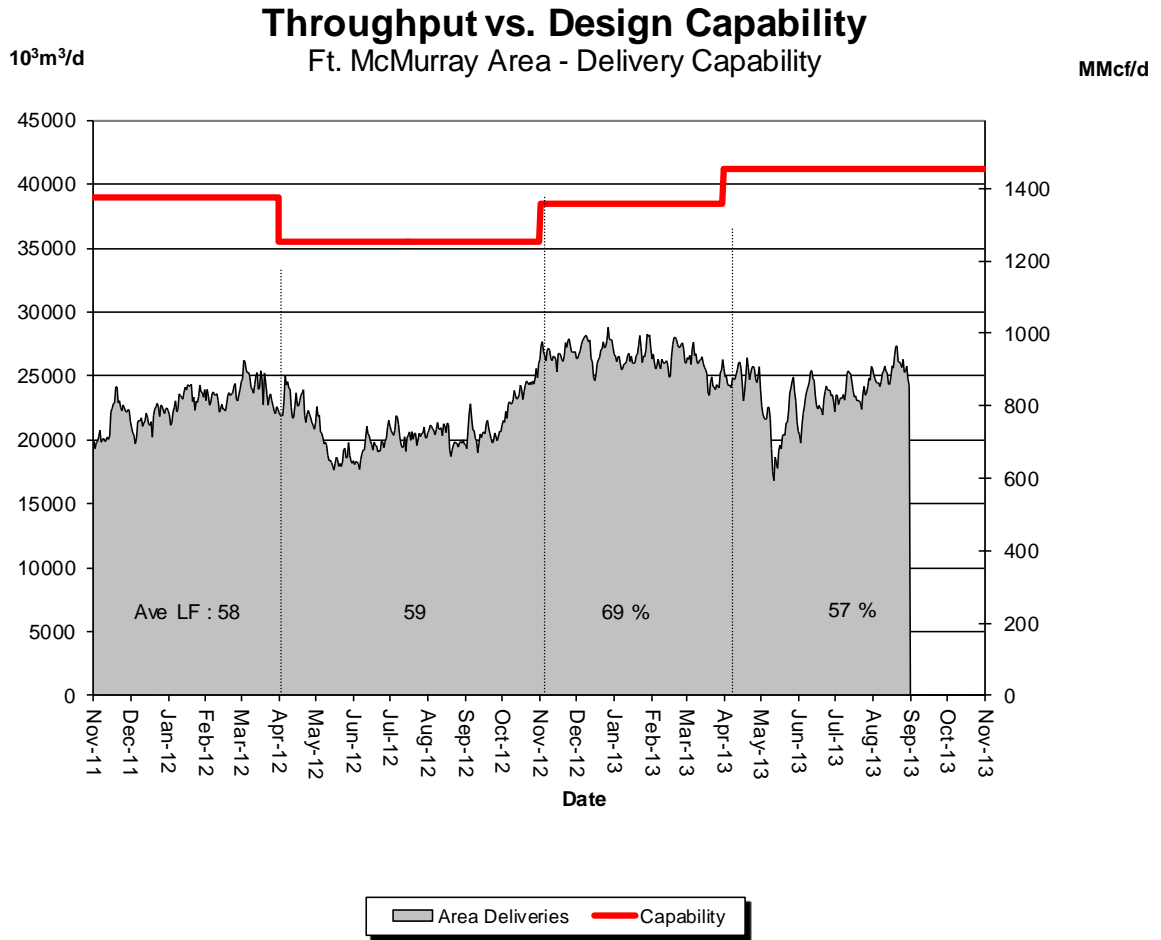



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	66	61	52	56	58	62

DESIGN CAPABILITY UTILIZATION KIRBY AREA – FLOW WITHIN

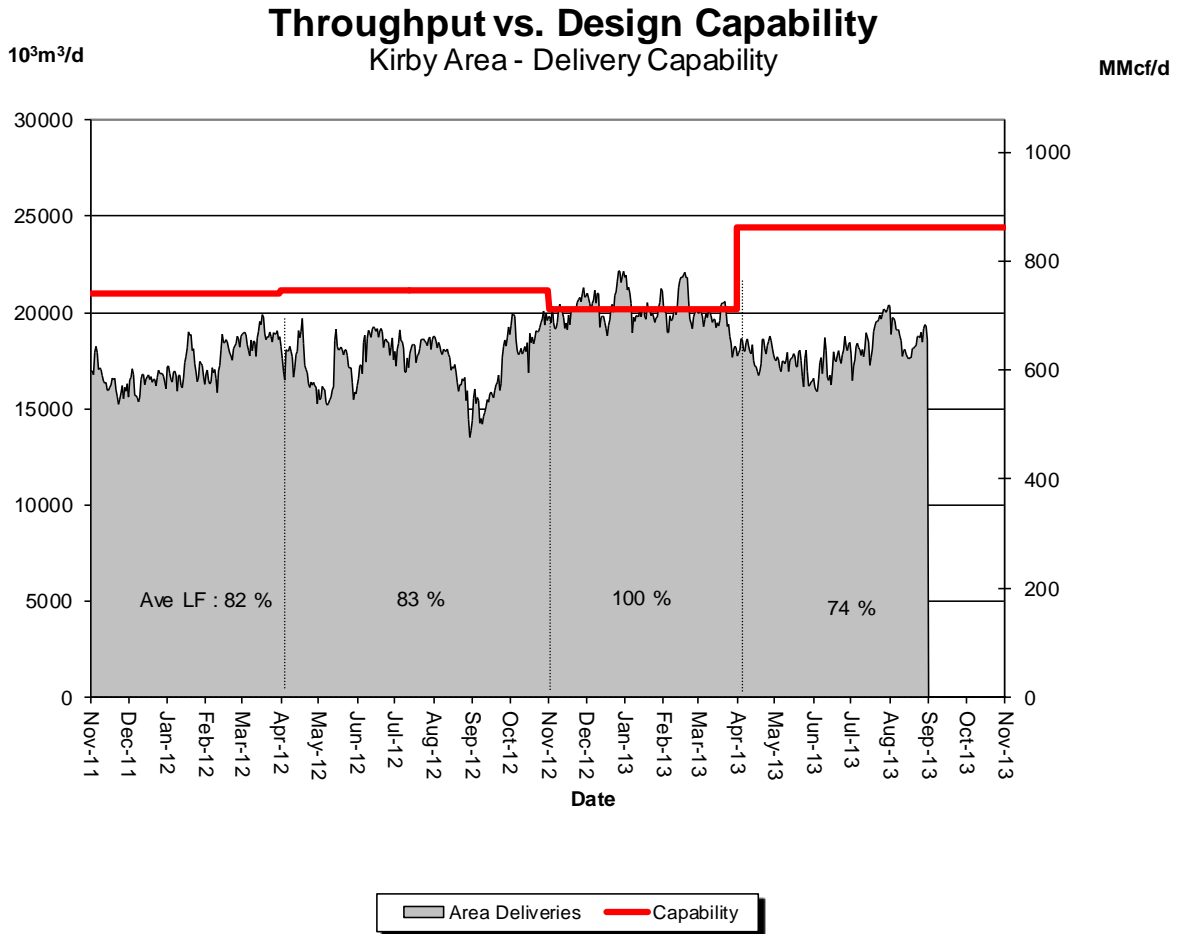



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	97	73	71	71	76	76

DESIGN CAPABILITY UTILIZATION NORTH OF BENS LAKE – FLOW WITHIN

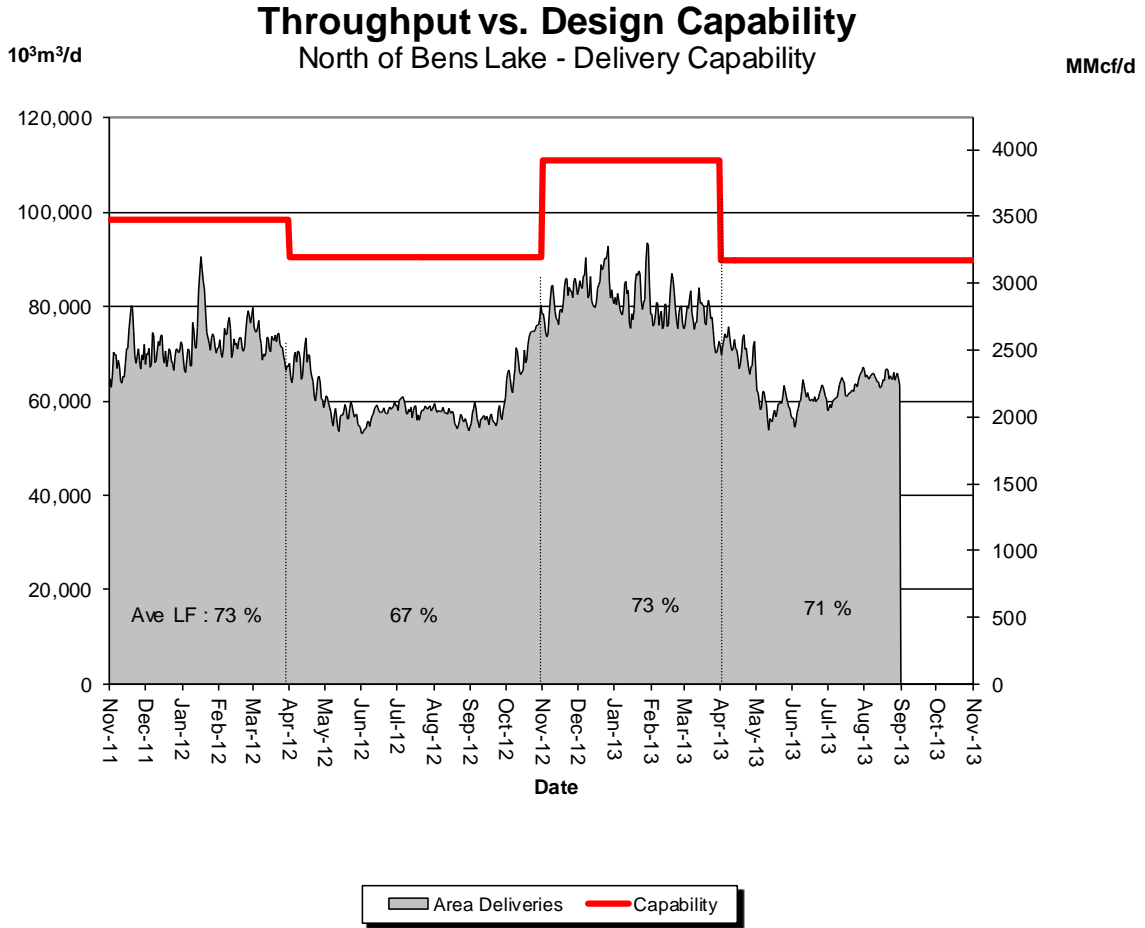



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	70	79	67	67	71	72

DESIGN CAPABILITY UTILIZATION NORTH & SOUTH OF BENS LAKE – FLOW WITHIN

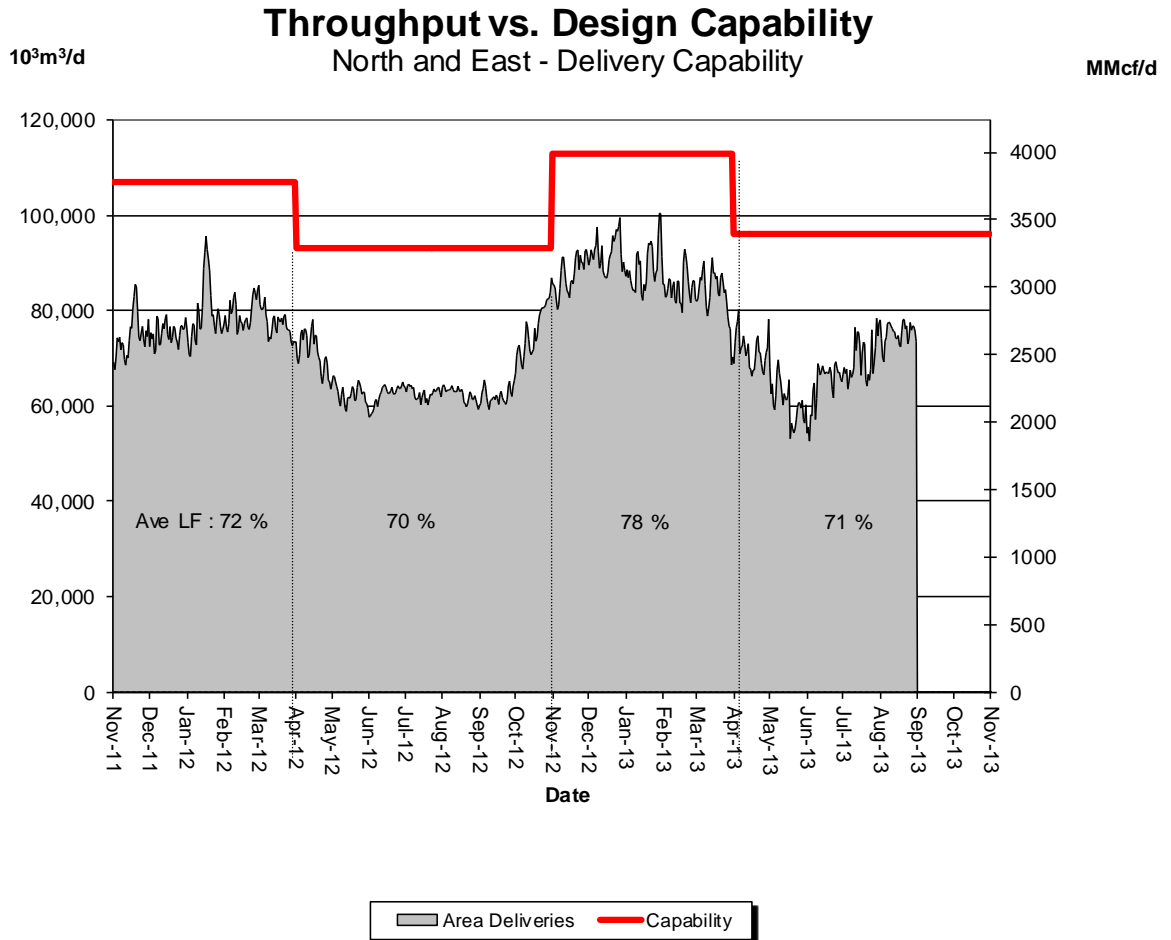



% Design Capability Utilization						
Monthly Average Actual Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	74	75	64	67	74	78

DESIGN CAPABILITY UTILIZATION UPPER PEACE RIVER

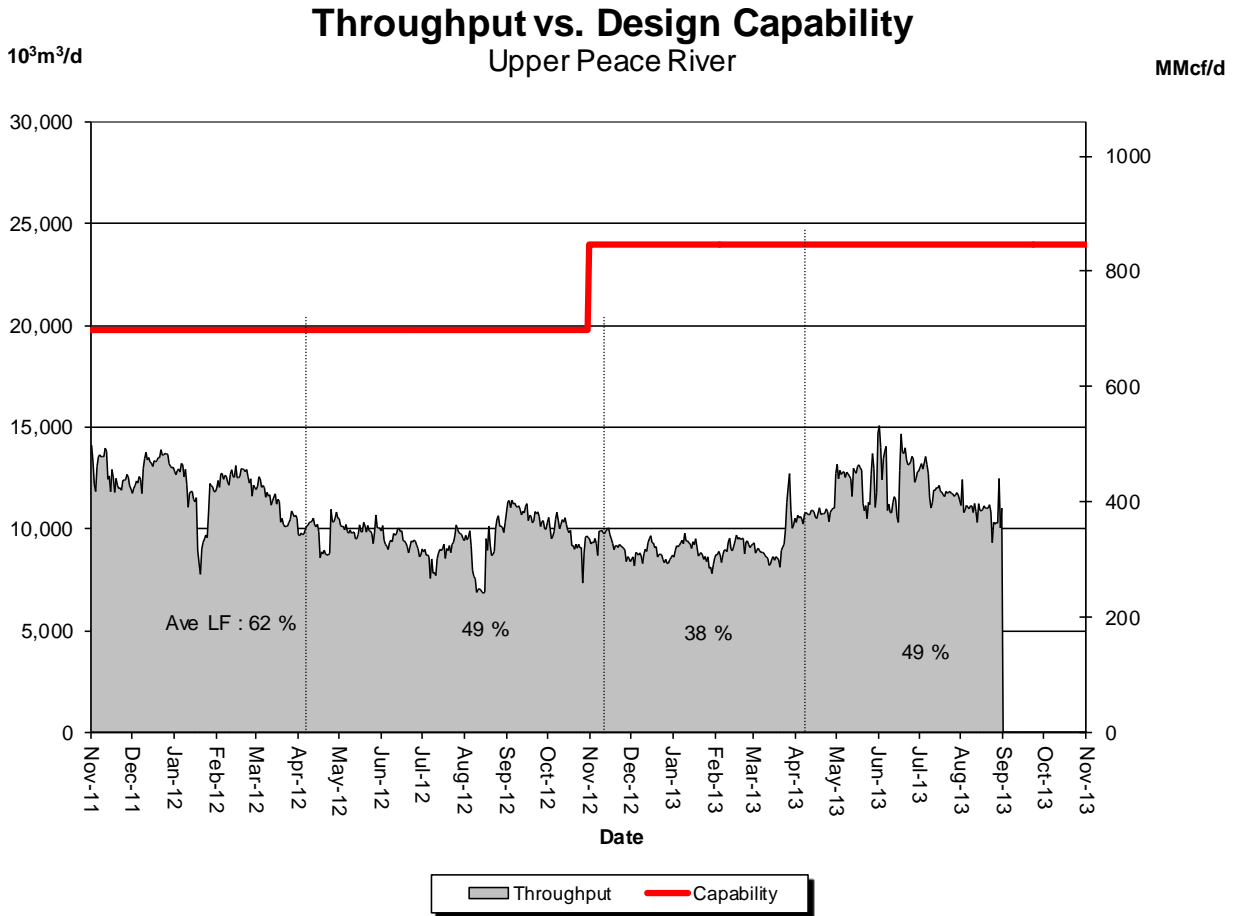

% Design Capability Utilization						
Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	39	45	51	53	50	45


DESIGN CAPABILITY UTILIZATION UPPER and CENTRAL PEACE RIVER

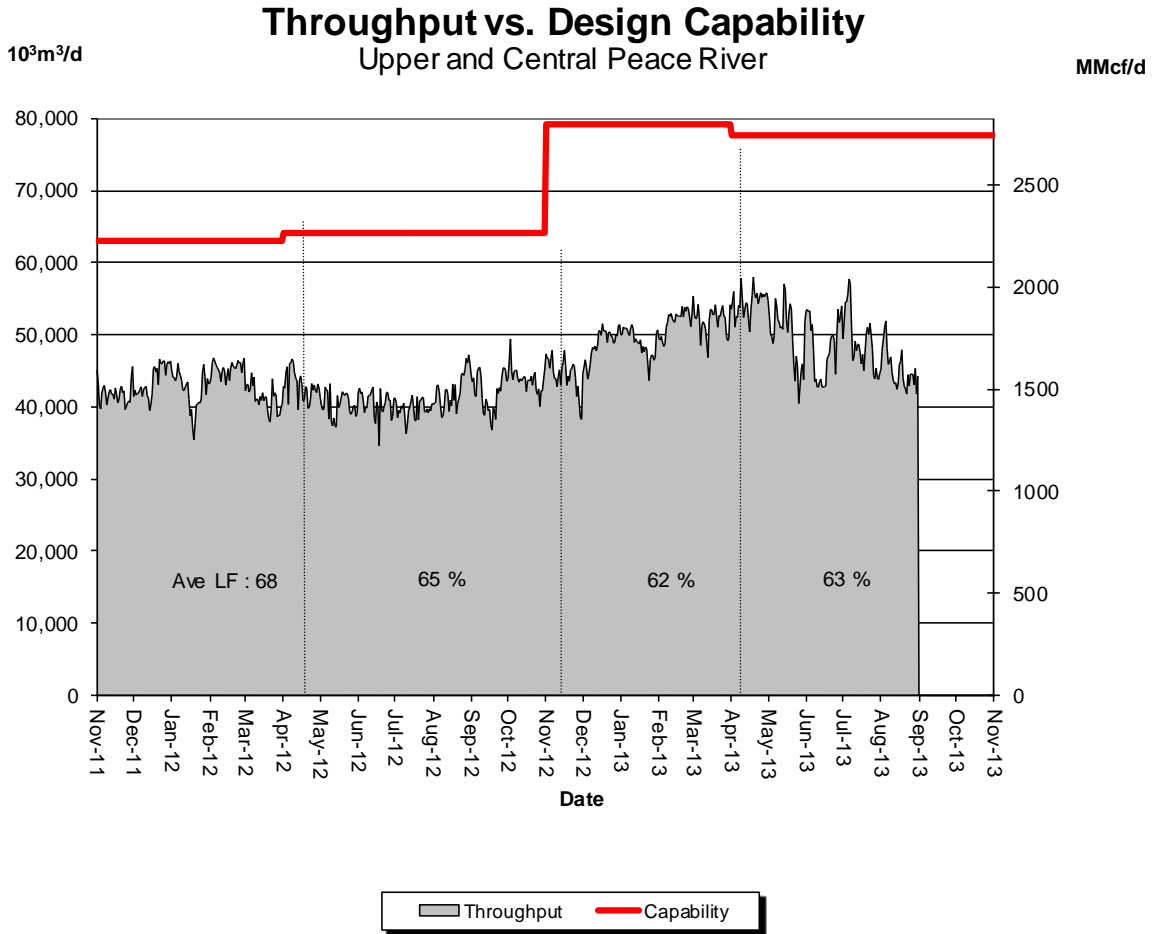



% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Capacity						
Average Flow/ Design Capacity	Mar	Apr	May	Jun	Jul	Aug
	66	70	64	62	63	58

DESIGN CAPABILITY UTILIZATION PEACE RIVER DESIGN

(Upper, Central and Lower Peace River)





Throughput vs. Design Capability Peace River Design

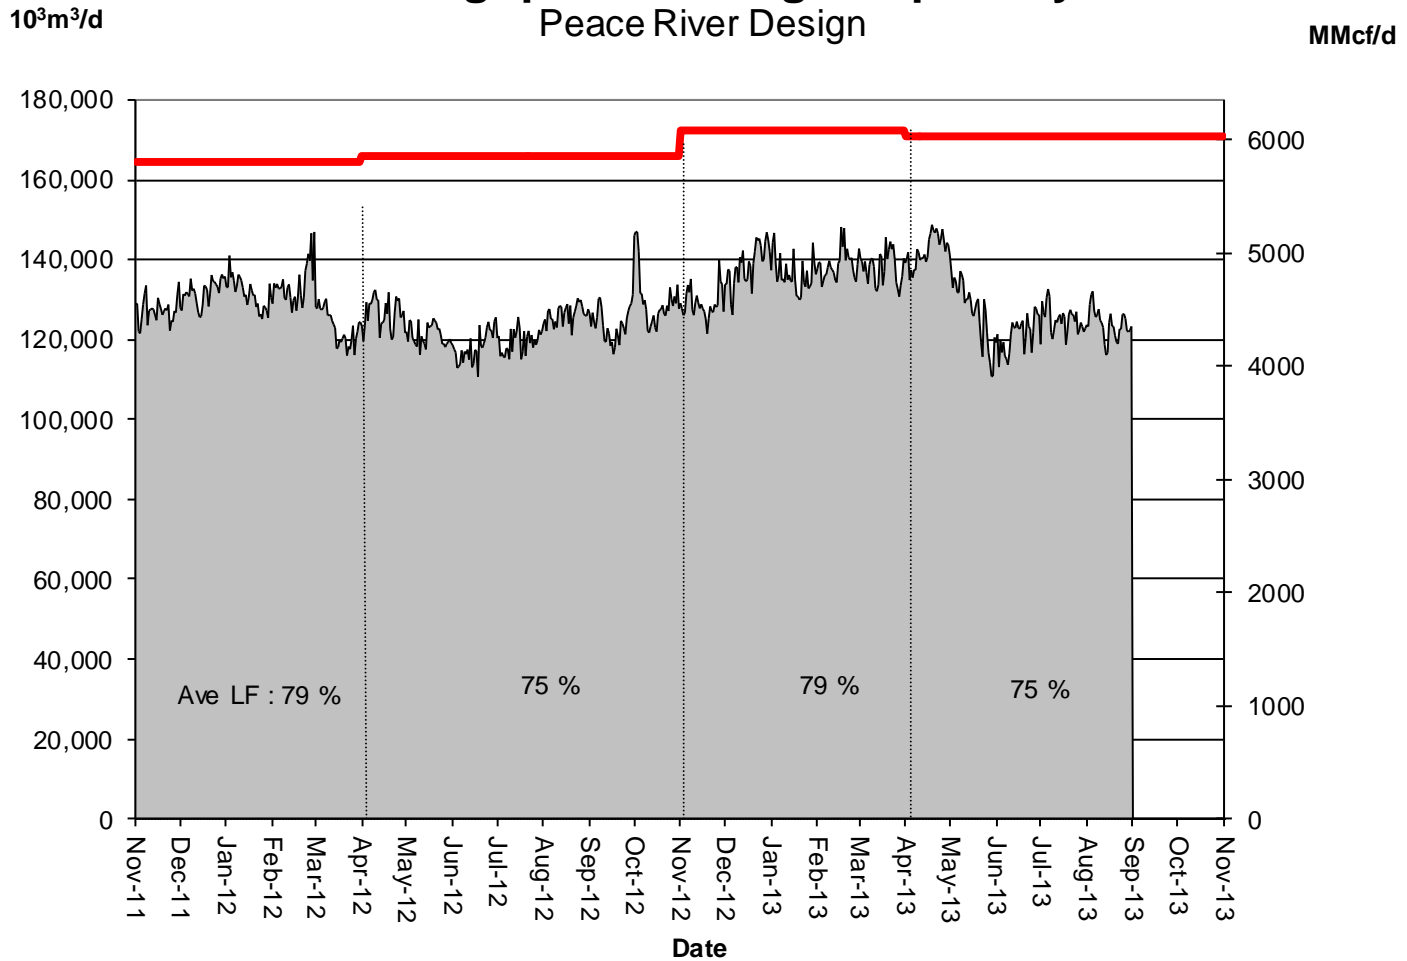

% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	80	83	75	71	73	72



DESIGN CAPABILITY UTILIZATION UPSTREAM JAMES RIVER

(Edson Mainline, Peace River Design and Marten Hills)

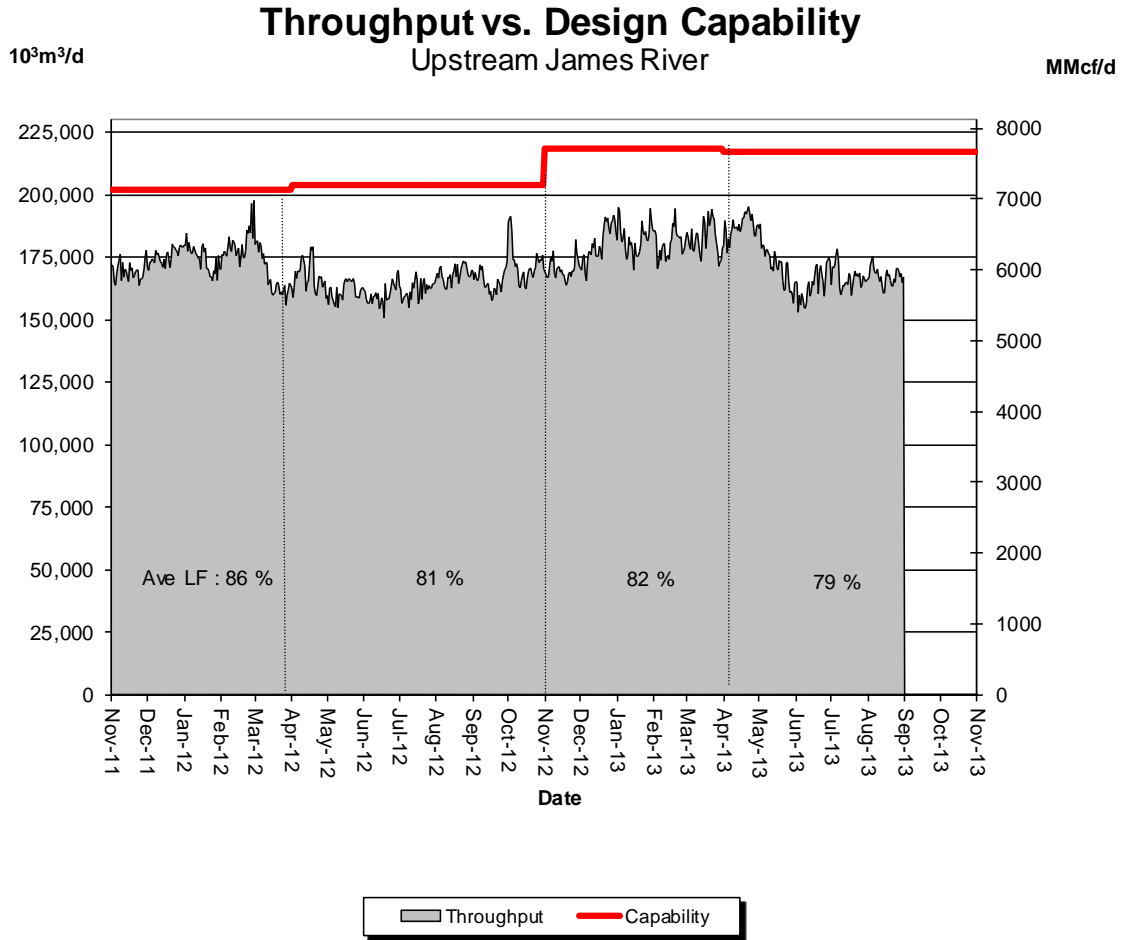



% Design Capability Utilization						
Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar 84	Apr 87	May 79	Jun 76	Jul 77	Aug 77

DESIGN CAPABILITY UTILIZATION SOUTH and ALDERSON – FLOW WITHIN

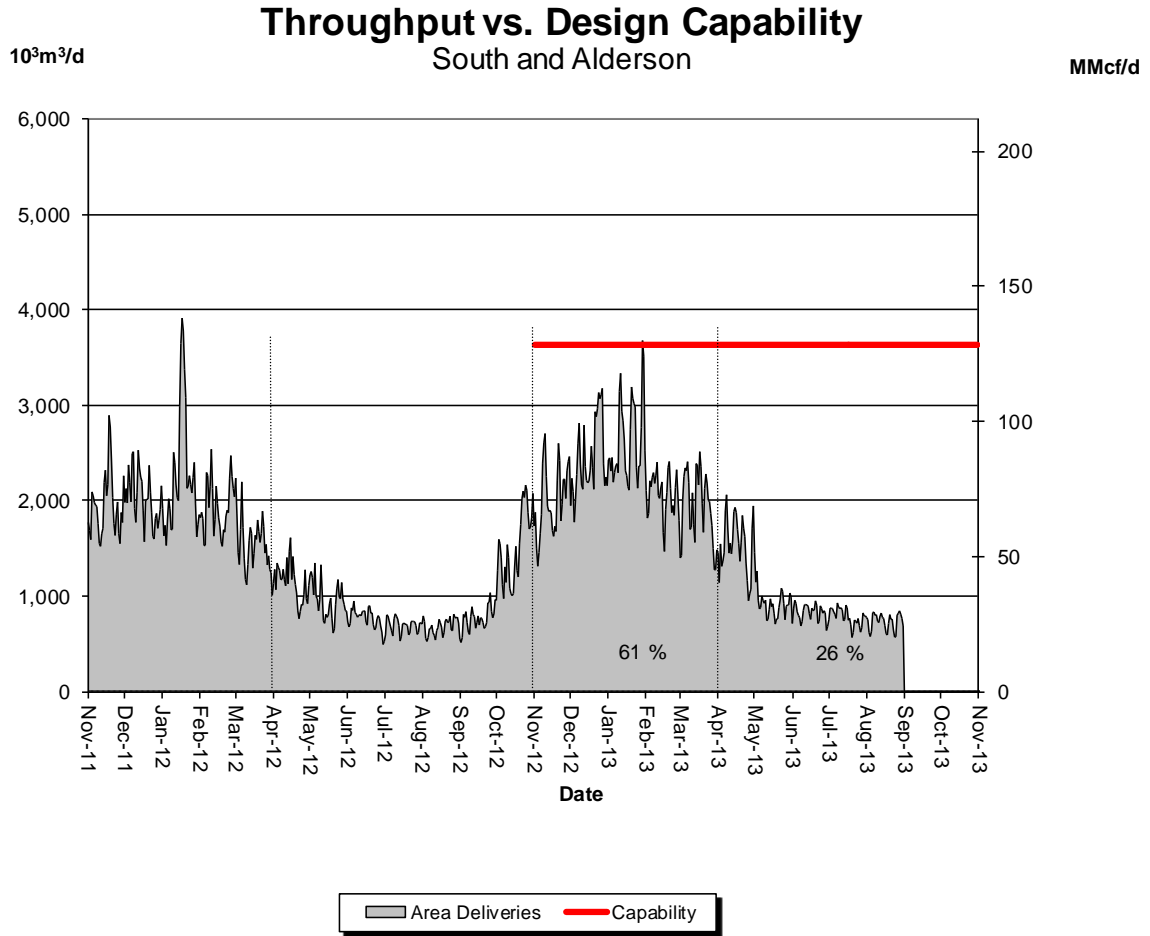



% Design Capability Utilization						
Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	53	42	28	23	22	20

DESIGN CAPABILITY UTILIZATION RIMBEY-NEVIS – FLOW WITHIN

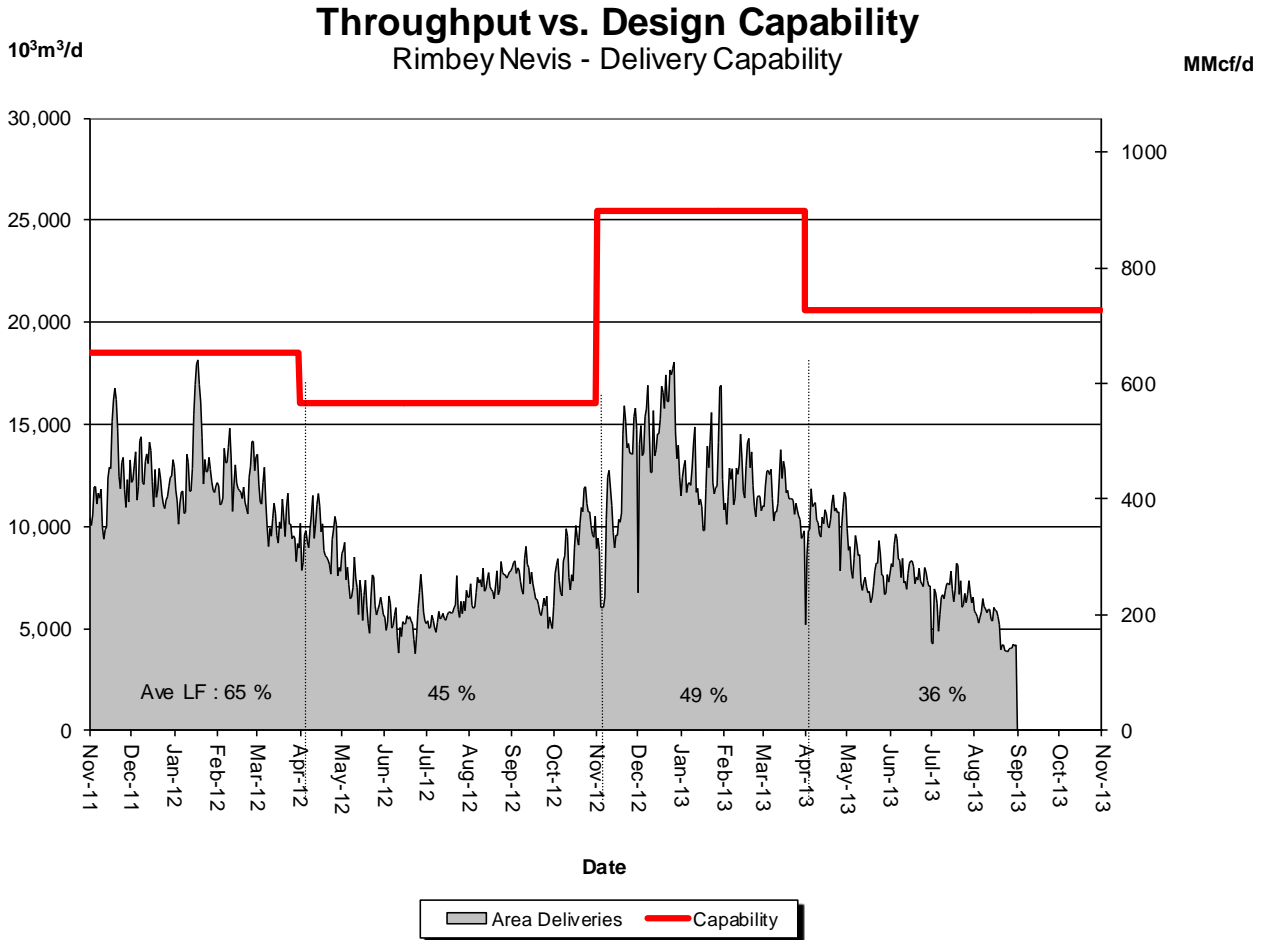



% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	47	51	39	38	33	25

DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE (James River to Princess)

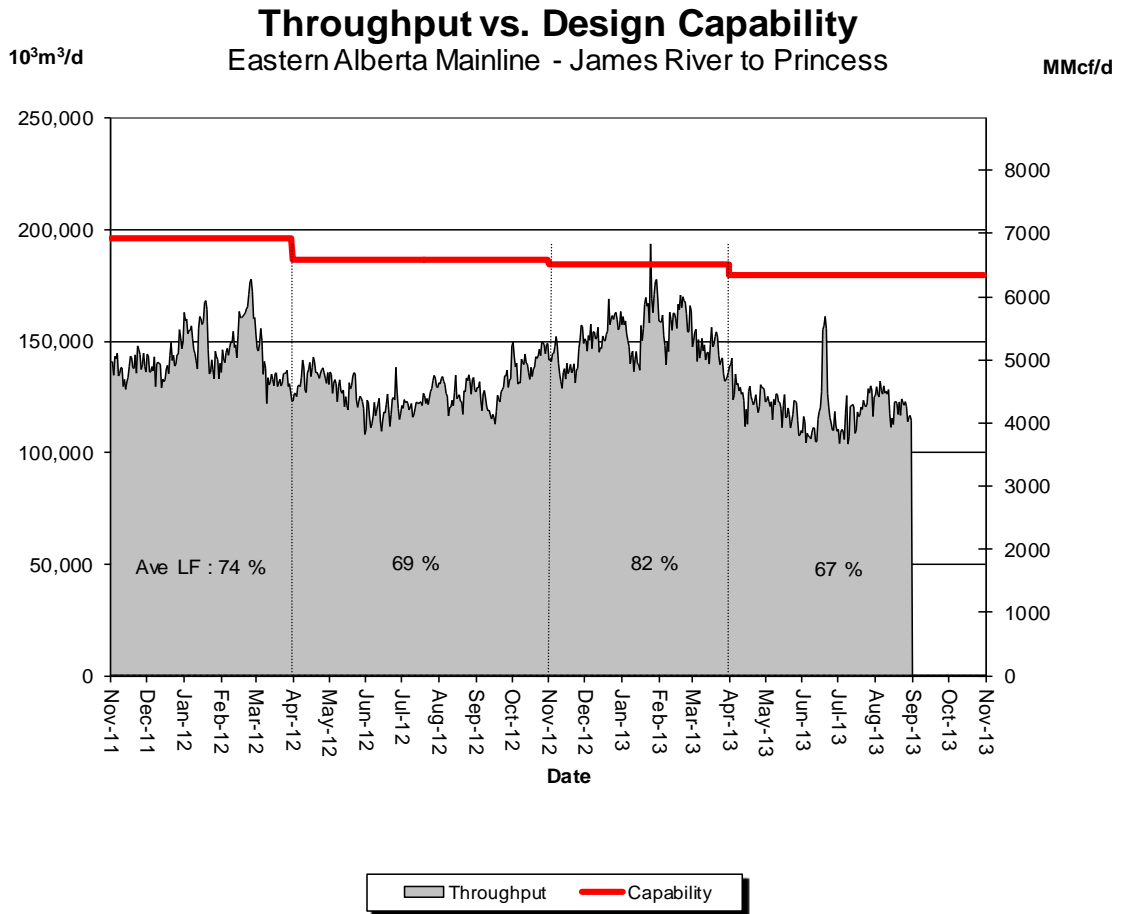

% Design Capability Utilization						
Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	79	70	67	66	66	68




DESIGN CAPABILITY UTILIZATION MEDICINE HAT – FLOW WITHIN

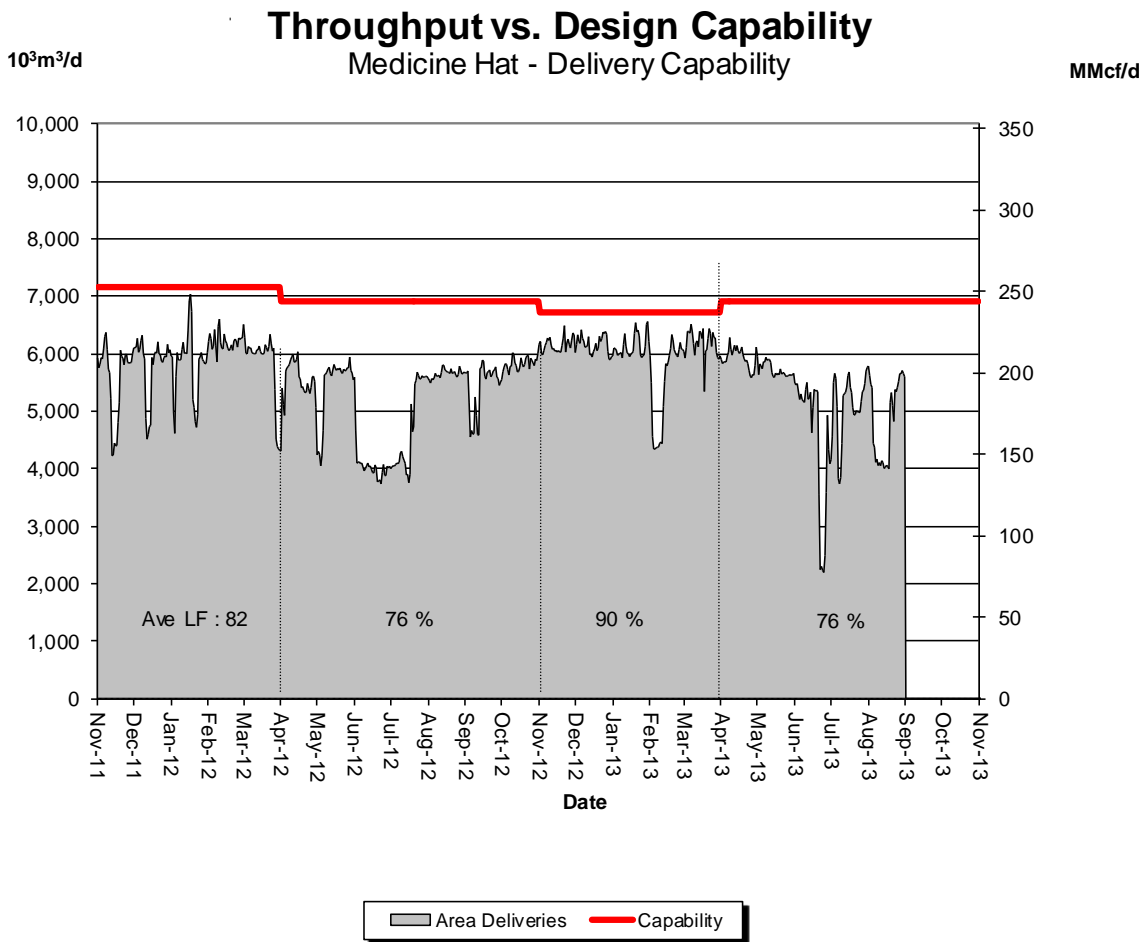

% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Mar	Apr	May	Jun	Jul	Aug
	92	86	83	66	74	70



DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE

(Princess to Empress / McNeill)

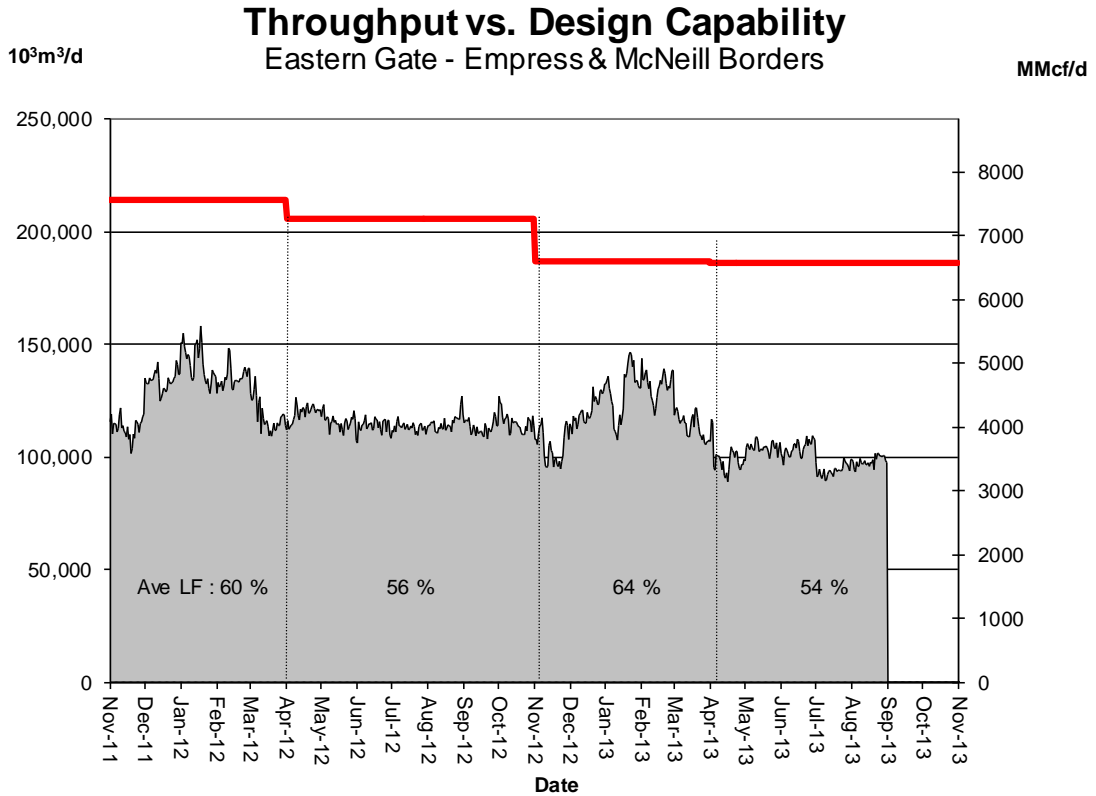

% Design Capability Utilization Average Actual Flow as a Percentage of Design Capability						
Average Flow / Design Capability	Mar	Apr	May	Jun	Jul	Aug
	61	53	56	56	51	53

DESIGN CAPABILITY UTILIZATION WESTERN ALBERTA MAINLINE (Alberta/B.C. and Alberta/Montana Borders)

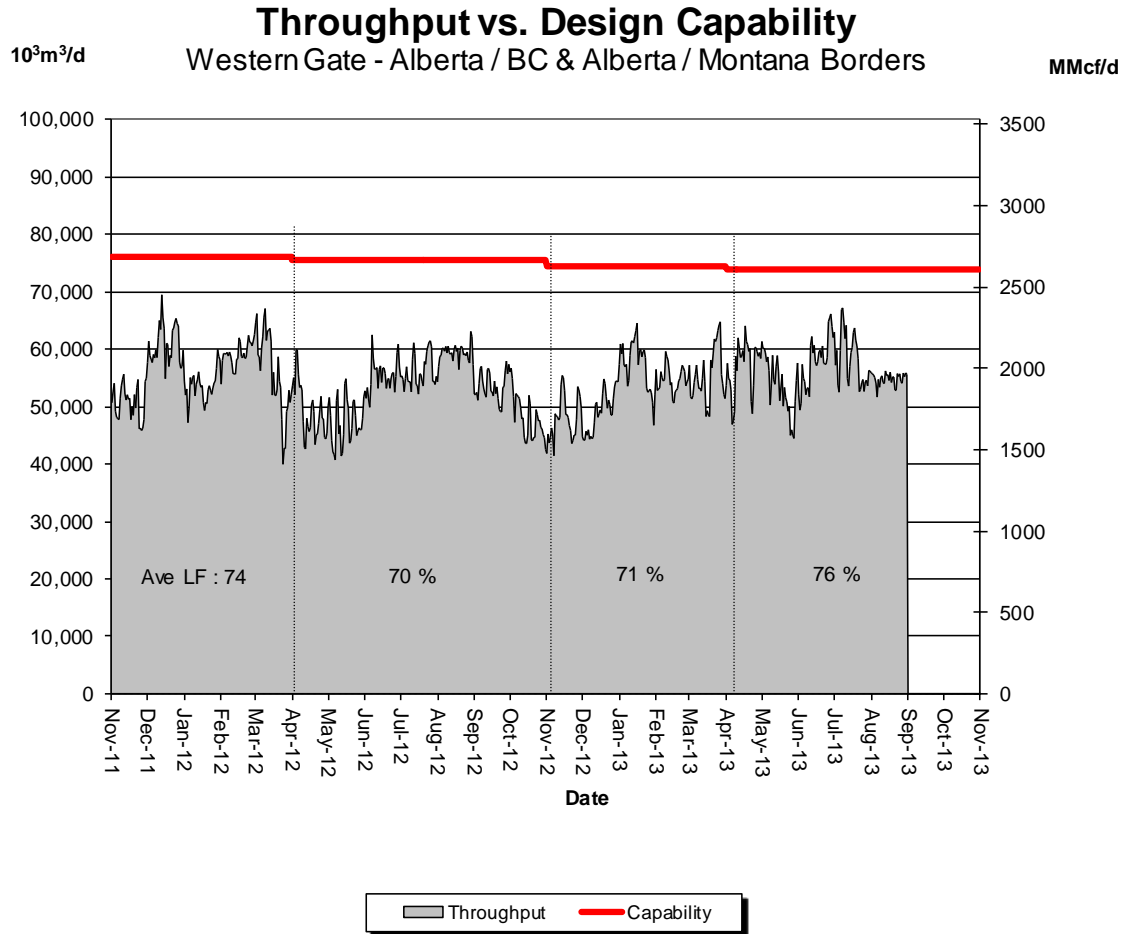

% Design Capability Utilization Average Actual Flow as a Percentage of Design Capability						
Average Flow / Design Capability	Mar	Apr	May	Jun	Jul	Aug
	74	77	73	78	79	74

FUTURE FIRM TRANSPORTATION SERVICE AVAILABILITY (MAINLINE RESTRICTIONS)

Receipt and Delivery Firm Transportation Guidelines

Firm Transportation Location	Authorize Firm Transportation Service By	To Ensure Firm Transportation Service By
Summer construction (generally south of Edmonton)	November 2013	November 2015
Winter construction (generally north of Edmonton)	November 2013	April 2016

Estimated Firm Transportation Service Availability

Please refer to the following web site for
current FT-R / FT-D Availability Maps:

<http://www.transcanada.com/customerexpress/2801.html>

➤ If your needs for firm transportation service arise after the above dates to “Authorize Firm Transportation Service By”, NGTL will evaluate your new receipt firm transportation service or firm service transfer requests on a date-stamped basis.

Please consult with your Customer Sales Representative to discuss your Firm Transportation Service needs.

HOW TO USE THIS REPORT

Overview

This report contains recent historical information on the level of utilization of firm transportation Service Agreements on the NGTL system, relative usage of interruptible service, level of utilization of design pipeline capacity, and the availability of transportation services as an indication of system reliability.

Data is reported either by *Pipeline Segment* (26 on the system) or *Design Area* (13 on the system). Maps of both are included in the reference section.

Firm Transportation Service Contract Utilization

The Firm Transportation Service Contract Utilization report shows the percent utilization for each of the 26 NGTL pipeline segments and 3 major export delivery points comprising the total system. The utilization data is based on billed monthly volumes. Percent utilization is calculated as firm transportation service and firm transportation service + interruptible service divided by applicable receipt or delivery contract level. Historical Data involving billed volumes lags the current date by approximately two months.

Design Capability Utilization

The load factor/segment flow graphs show actual flow versus design capability values for various NGTL system areas. The graphs also show seasonal (winter/summer) design capability and average load factors for each season. Data used in these reports lags the current date by one month.


Design Flow Capability utilization is a function of several factors that include:

- Total market demand for Alberta natural gas.
- Seasonal changes in market demand for Alberta natural gas.
- Receipt nominating practices of customers individually and in aggregate to meet that level of demand.
- Effect of scheduled maintenance on actual flow requirement in a design area at any given time.
- Design assumptions used in determining required segment flow requirement.

Future Firm Transportation Service Availability


The Future Firm Transportation Service Availability report presents guidelines and timing for all future firm transportation service requests.

NGTL Design Areas

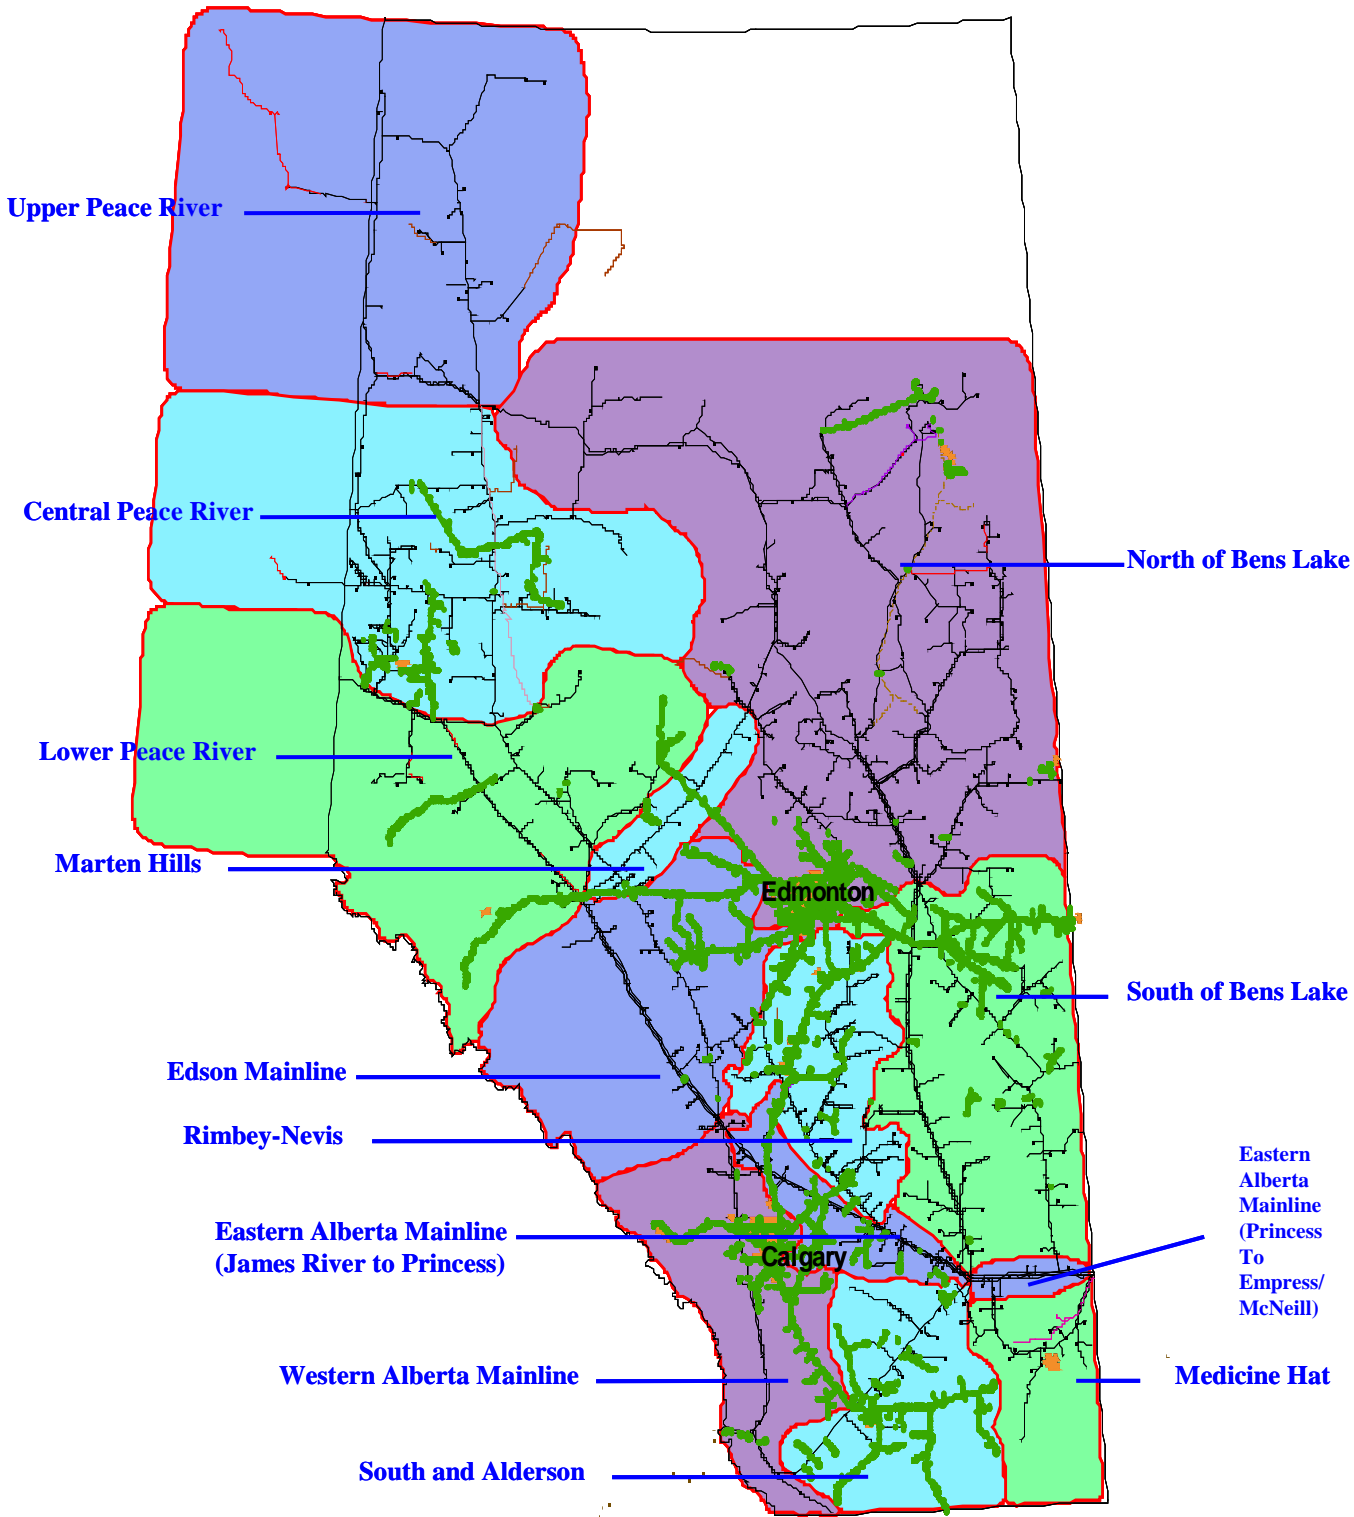

(Last updated Nov 2011)

NGTL Pipeline Segments

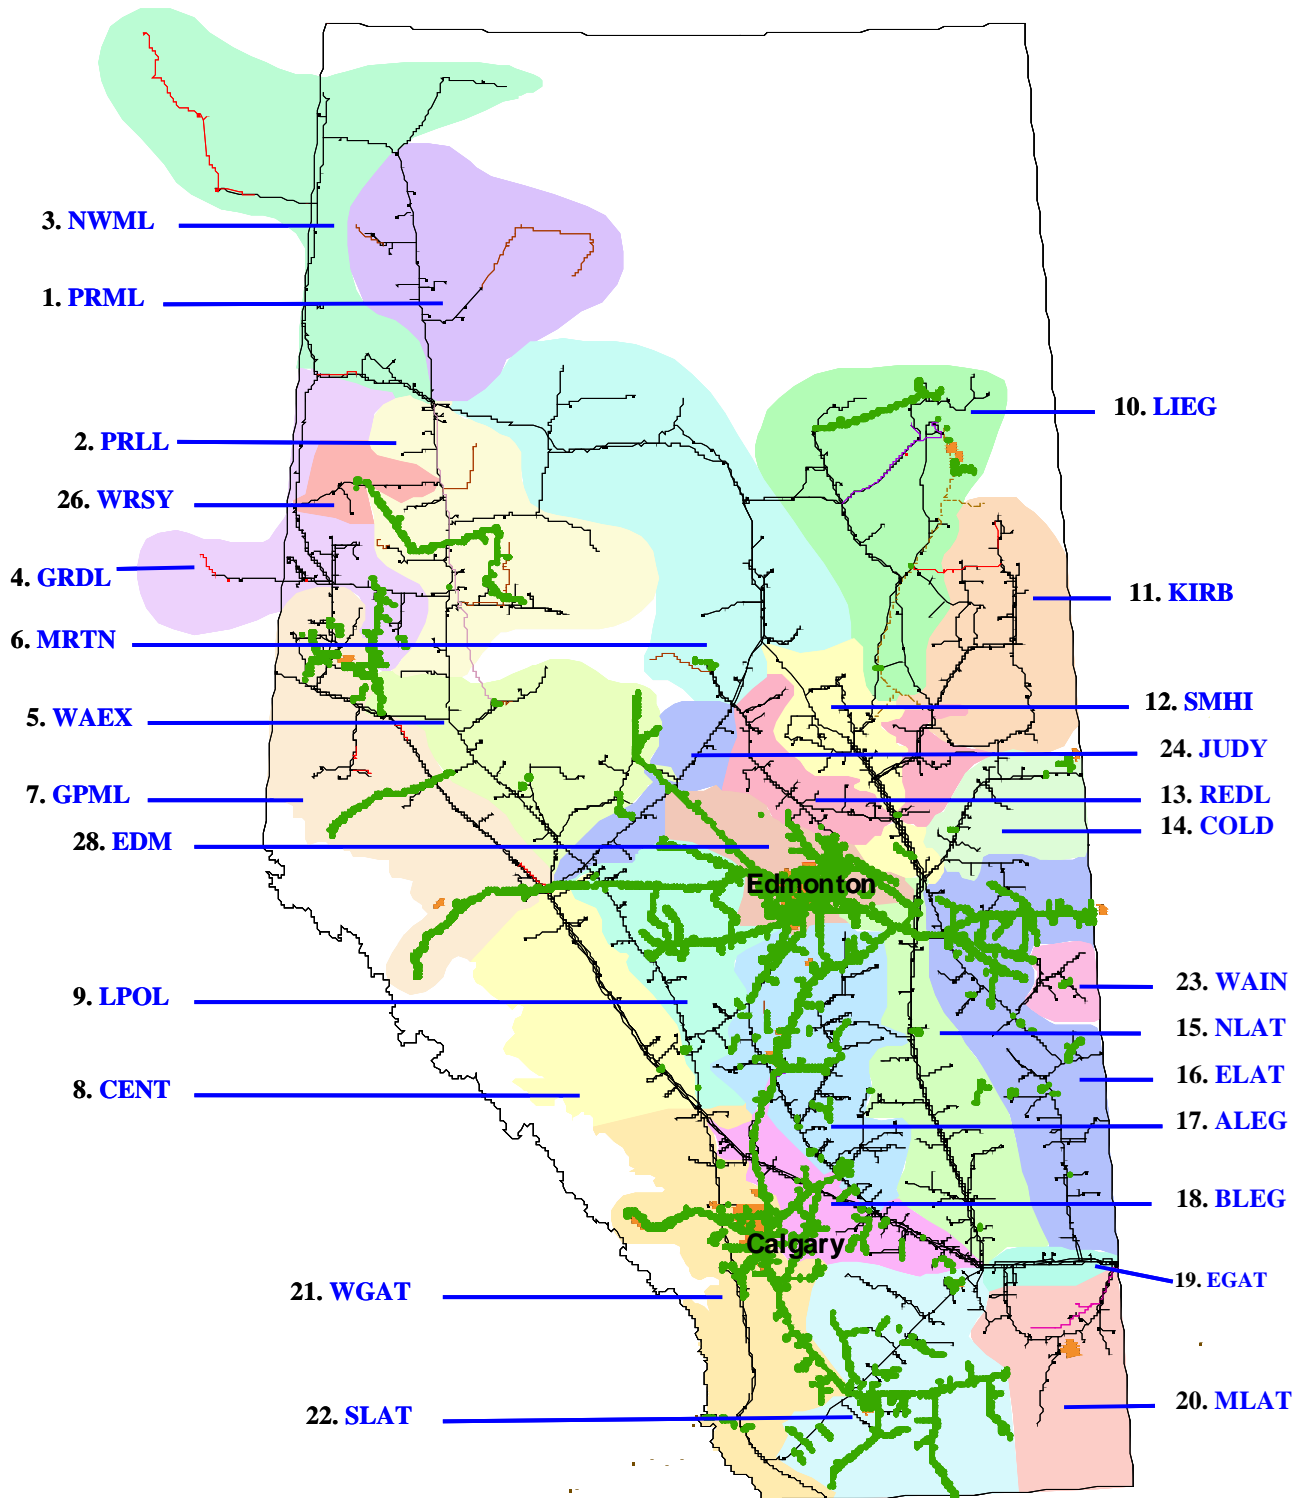

(Last updated Nov 2011)

DEFINITION OF TERMS

Design Capability Utilization

Actual Flow

The amount of gas flowing within or out of our design area.

Design Capability

The volume of gas that can be transported at various points on the pipeline system considering design assumptions.

AVGLF (Average Load Factor)

The ratio between average *Actual Flow* and *Design Capability*. It is calculated for every design season (summer/winter) as shown on the graphs.

Intra-Alberta Deliveries

The amount of sales gas flowing off the system within an area.

Receipt Flow

Aggregate of actual receipts within an area and the *Actual Flow* of the upstream area.

Historical Transportation Service Availability

Average % CD Restricted

The average percentage of the entire segment receipt contract demand restricted during periods of restriction.

Firm Service Available

The percentage of time that all requested firm transportation service requests were transported within a segment.

Firm Service Restriction

Percentage of time firm service is restricted.

IT-2 Service Available

The percentage of time that IT-2 service requests were transported.

Max % CD Restricted

The maximum percentage to which the entire segment contract demand was restricted.

Other

System Load Factor

The volume weighted average of the *Average Load Factor (AVGLF)* of all design areas on the system
