

SYSTEM UTILIZATION AND RELIABILITY MONTHLY REPORT

for the month ending
February 2013

<http://www.transcanada.com/customerexpress/2885.html>

Published date:
May 5, 2013

Highlights This Month:

- The average actual flow for the dominant flow condition in each of the Alberta design areas is compared against the corresponding design capability to obtain a measure of pipeline utilization. Consequently, design capability utilization is measured as Average Actual Flow / Seasonal Design Capability.
- FT Receipt Availability over a 3 month average from December 1, 2012 – February 28, 2013 was deemed to be 100% available in all pipe segments.
- Border Availability at Empress/McNeill, Gordondale and Alberta/BC, over a 3 month average from December 1, 2012 – February 28, 2013 were all deemed 100% available.
- The Firm Transportation service contract utilization table (page 3 of this report) illustrates the FT and FT + IT utilization for receipts and deliveries.
- Design methodology for The Marten Hills Area is currently being reviewed. The chart currently displays up to date throughput without a corresponding Capability value.

NOVA Gas Transmission Ltd.

TABLE OF CONTENTS

<u>MONTHLY FEATURES</u>	PAGE
Firm Transportation Service Contract Utilization	3
Design Capability Utilization	
Ft. McMurray Area – Flow Within.....	4
Kirby Area – Flow Within.....	5
North of Bens Lake – Flow Within	6
North & South of Bens Lake – Flow Within.....	7
Upper Peace River	8
Upper & Central Peace River	9
Peace River Design	10
Marten Hills	11
Upstream James River	12
South & Alderson – Flow Within	13
Rimbey Nevis – Flow Within	14
Eastern Alberta Mainline (James River to Princess)	15
Medicine Hat - Flow Within	16
Eastern Alberta Mainline (Princess to Empress/McNeill)	17
Western Alberta Mainline (AB/BC & AB/Montana Borders)	18
Historical Transportation Service Availability (3 Month Average)	19
Future Firm Transportation Service Availability.....	20
How to Use This Report	21

REFERENCES

NGTL Design Areas Map	23
NGTL Pipeline Segments Map	24
Definition of Terms	25

If you have any questions on the content of this report, contact Winston Cao at (403) 920-5315 or via fax at (403) 920-2357.

FIRM TRANSPORTATION SERVICE¹ CONTRACT UTILIZATION³

By NGTL Pipeline Segments

February 2013

Segment	Contract	Delivery		Receipt	
		Utilization	Feb CD (TJ/d)	Utilization	Feb CD (MMcf/d)
UPRM	FT	3%	25.4	87%	68
	FT + IT ²	8%		96%	
LPRM	FT	0%	0.0	0%	0
	FT + IT	0%		0%	
PRL	FT	47%	42.2	93%	120
	FT + IT	47%		100%	
NWML	FT	23%	5.0	42%	647
	FT + IT	66%		43%	
GRDL	FT	39%	3.9	81%	1,667
	FT + IT	41%		83%	
WRSY	FT	0%	0.0	83%	25
	FT + IT	0%		96%	
WAEX	FT	13%	15.4	72%	340
	FT + IT	43%		91%	
JUDY	FT	29%	46.1	91%	111
	FT + IT	31%		109%	
GPML	FT	39%	159.5	87%	3,045
	FT + IT	52%		93%	
CENT	FT	6%	10.4	96%	836
	FT + IT	11%		121%	
LPOL	FT	42%	81.8	94%	508
	FT + IT	58%		122%	
WGAT	FT	73%	3,326.9	88%	443
	FT + IT	76%		105%	
ALEG	FT	55%	316.6	97%	902
	FT + IT	73%		117%	
SLAT	FT	38%	169.2	96%	245
	FT + IT	39%		114%	
MLAT	FT	74%	262.1	86%	207
	FT + IT	78%		98%	
BLEG	FT	61%	142.8	96%	618
	FT + IT	62%		109%	
EGAT	FT	96%	4,165.0	95%	40
	FT + IT	120%		110%	
MRTN	FT	18%	38.8	83%	81
	FT + IT	26%		101%	
LIEG	FT	81%	1,144.8	66%	28
	FT + IT	94%		224%	
KIRB	FT	83%	805.1	74%	37
	FT + IT	98%		116%	
SMHI	FT	78%	12.0	84%	39
	FT + IT	87%		136%	
REDL	FT	76%	13.1	77%	48
	FT + IT	110%		113%	
COLD	FT	76%	55.7	67%	34
	FT + IT	125%		101%	
EDM	FT	55%	1,692.5	92%	68
	FT + IT	56%		128%	
NLAT	FT	48%	15.4	96%	146
	FT + IT	49%		124%	
WAIN	FT	37%	0.4	77%	8
	FT + IT	37%		155%	
ELAT	FT	81%	257.9	88%	145
	FT + IT	81%		118%	
TOTAL SYSTEM	FT	77%	12,808.4	86%	10,456
	FT + IT	89%		98%	



*NOTE:

1. FT includes all receipt and delivery Firm Transportation Services: FTR, FTRN, LRS, FTD1,

2. IT includes all receipt and delivery Interruptible Services: ITR, FRO, ITD1, ITD2, and FDO.



3. Utilization data is based on billed monthly volumes. Percent utilization calculated as FT and FT + billed volumes divided by applicable receipt or delivery Contract level.

DESIGN CAPABILITY UTILIZATION FT. McMURRAY AREA – FLOW WITHIN

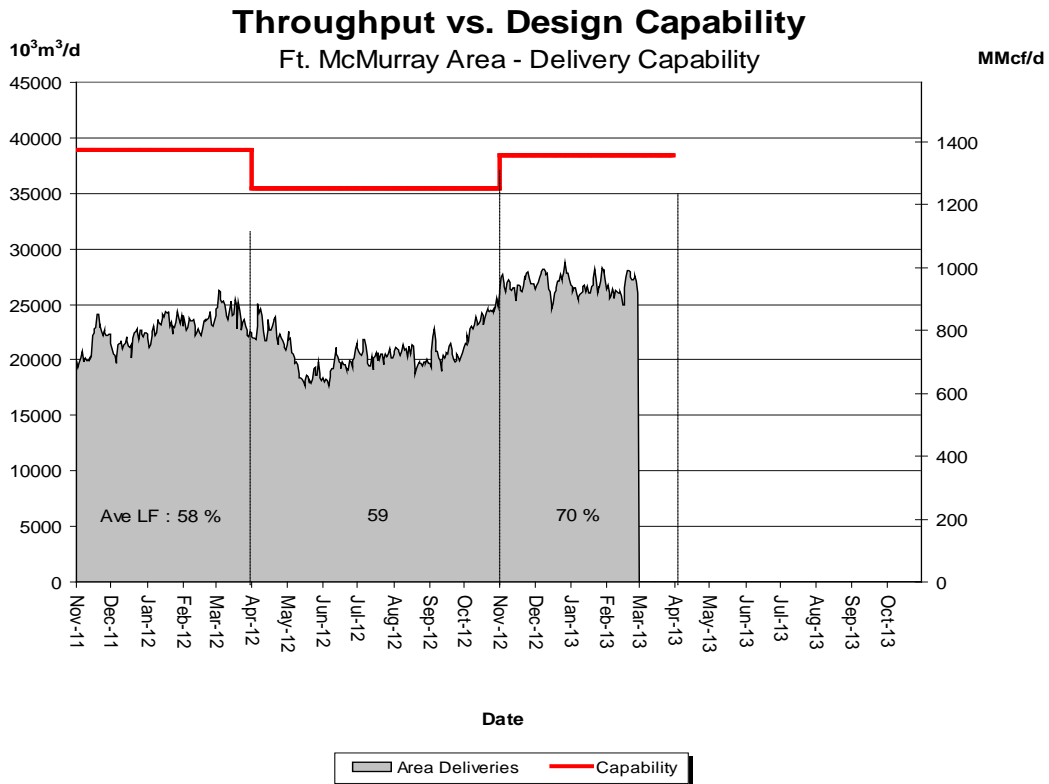



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep 58	Oct 66	Nov 70	Dec 70	Jan 69	Feb 69

DESIGN CAPABILITY UTILIZATION KIRBY AREA – FLOW WITHIN

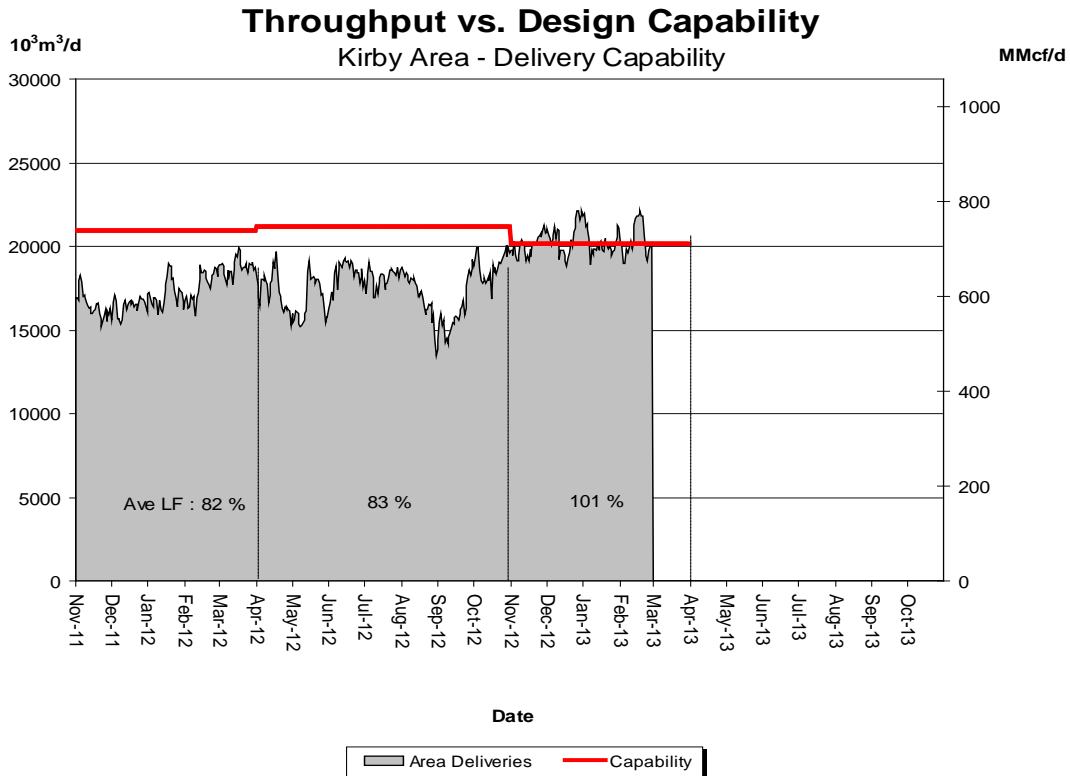



% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	76	89	99	102	101	101

DESIGN CAPABILITY UTILIZATION NORTH OF BENS LAKE – FLOW WITHIN

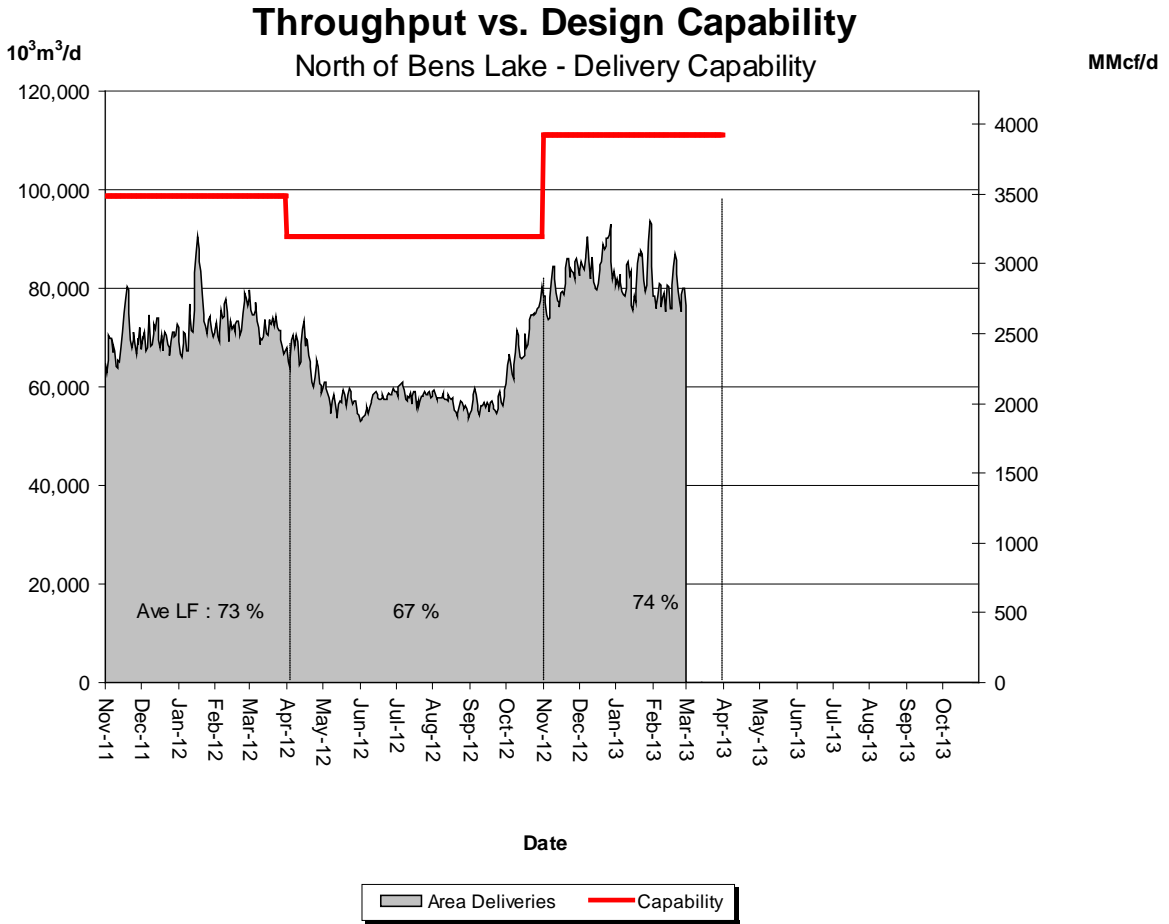



% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	62	77	73	77	75	71

DESIGN CAPABILITY UTILIZATION NORTH & SOUTH OF BENS LAKE – FLOW WITHIN

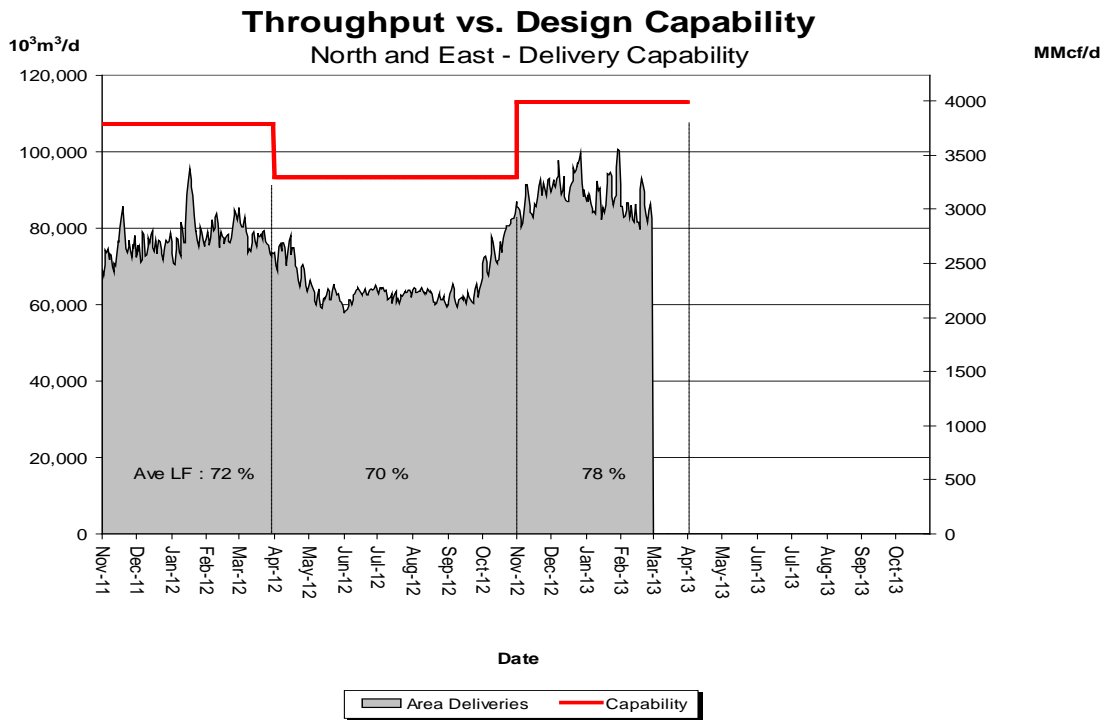



% Design Capability Utilization Monthly Average Actual Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	67	81	78	81	79	75

DESIGN CAPABILITY UTILIZATION UPPER PEACE RIVER

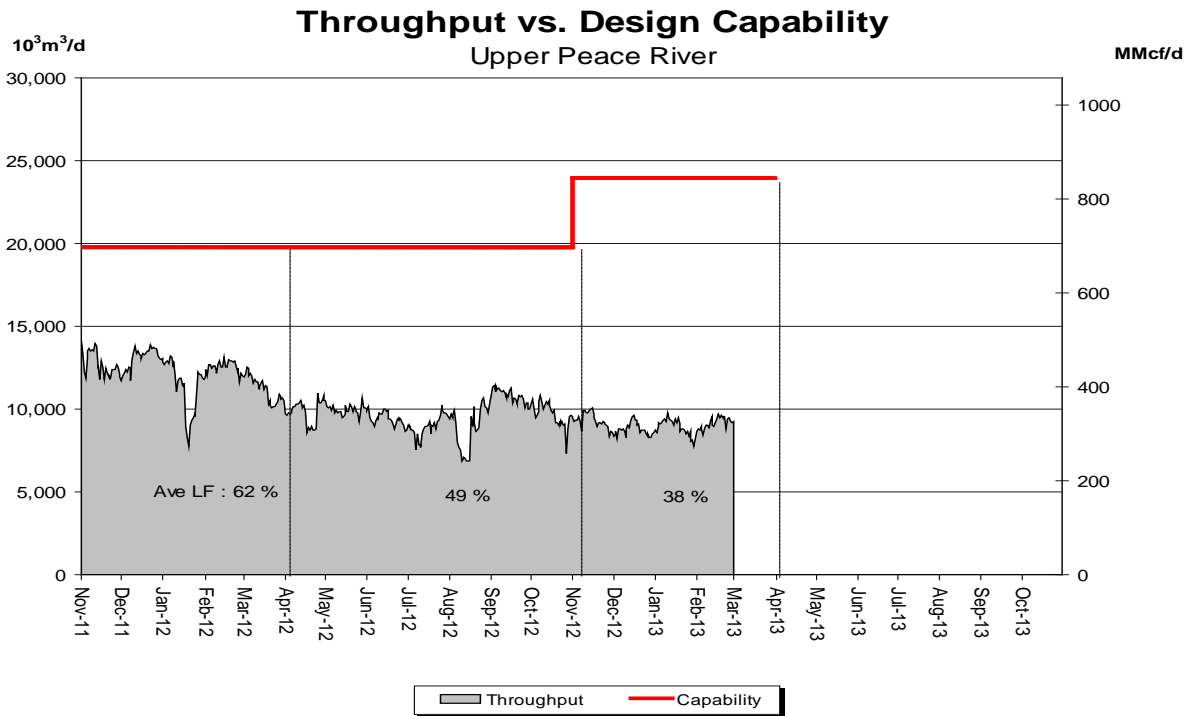



% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	55	49	39	37	37	38

DESIGN CAPABILITY UTILIZATION UPPER and CENTRAL PEACE RIVER

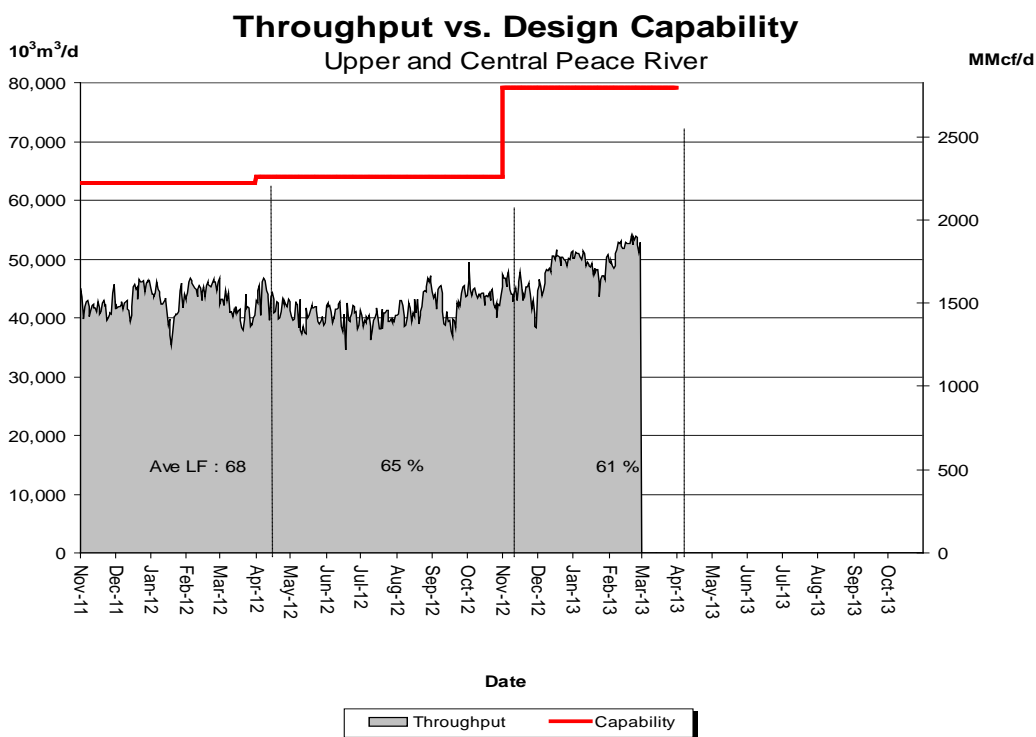



% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Capacity						
Average Flow/ Design Capacity	Sep	Oct	Nov	Dec	Jan	Feb
	66	68	56	61	62	65

DESIGN CAPABILITY UTILIZATION PEACE RIVER DESIGN (Upper, Central and Lower Peace River)

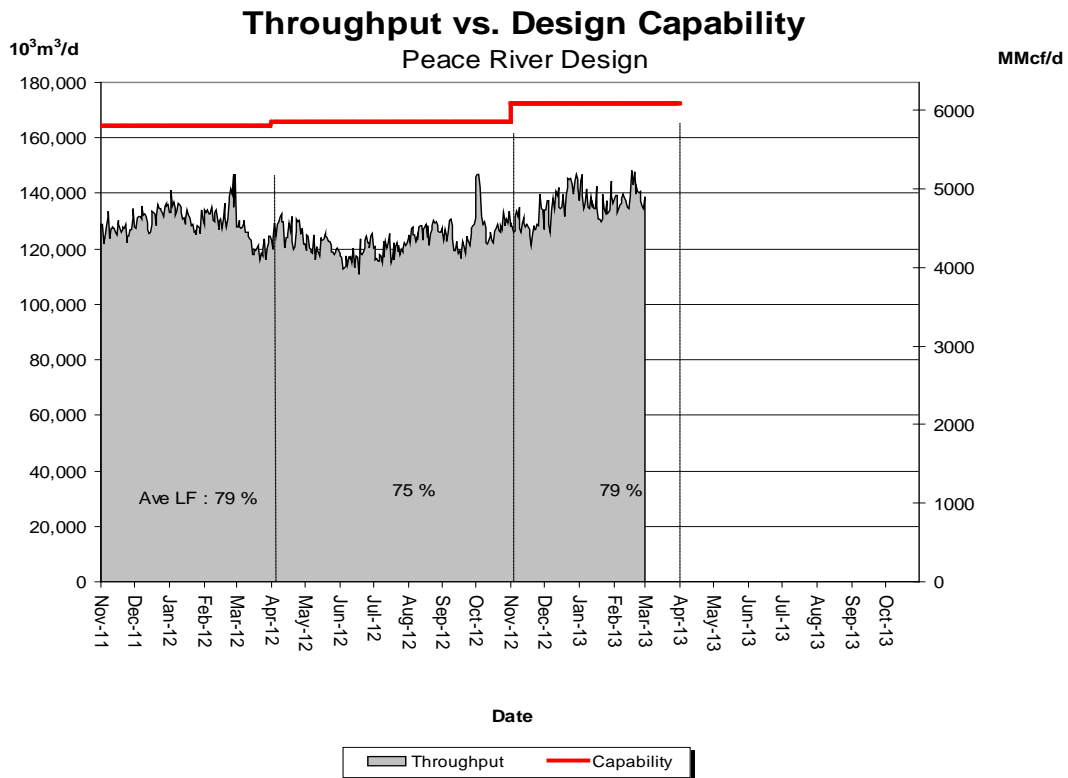



% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	75	78	75	80	79	81

DESIGN CAPABILITY UTILIZATION MARTEN HILLS

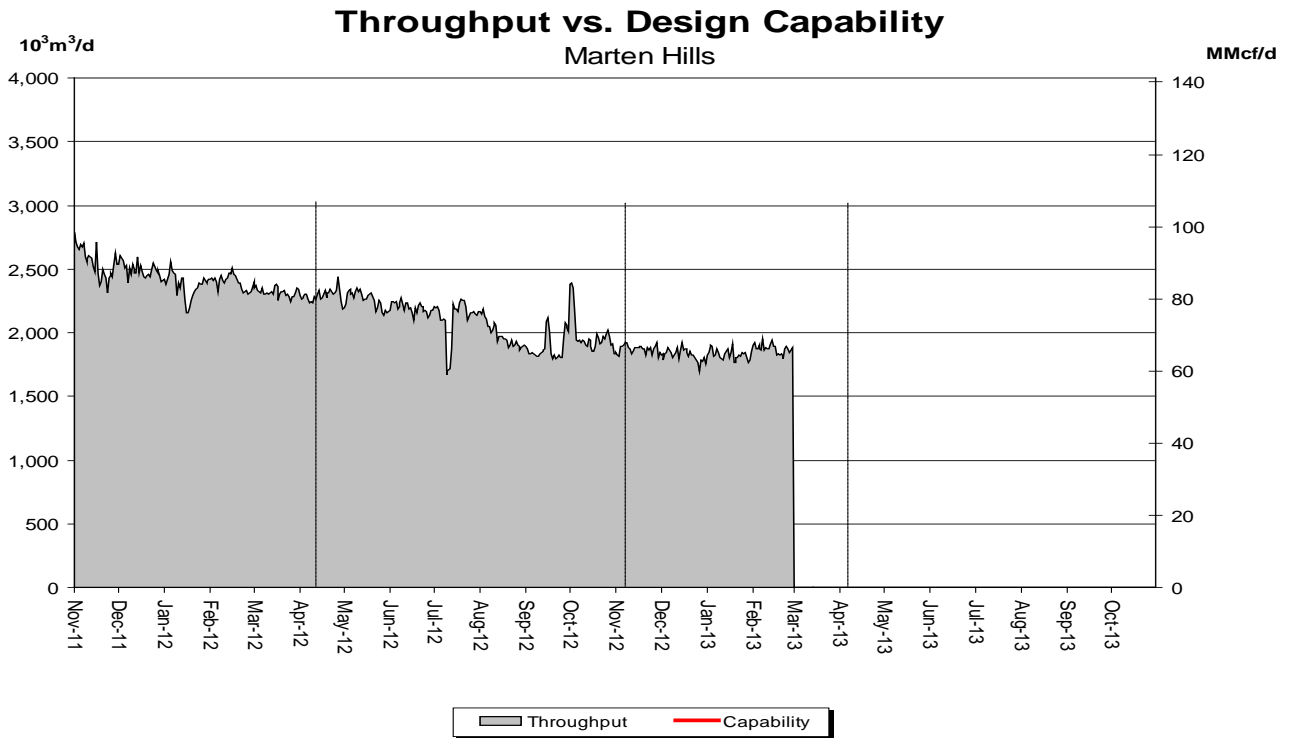



Design methodology for Marten Hills Area currently being reviewed.
 Chart currently displays up to date throughput without a corresponding Capability value.

DESIGN CAPABILITY UTILIZATION UPSTREAM JAMES RIVER (Edson Mainline, Peace River Design and Marten Hills)

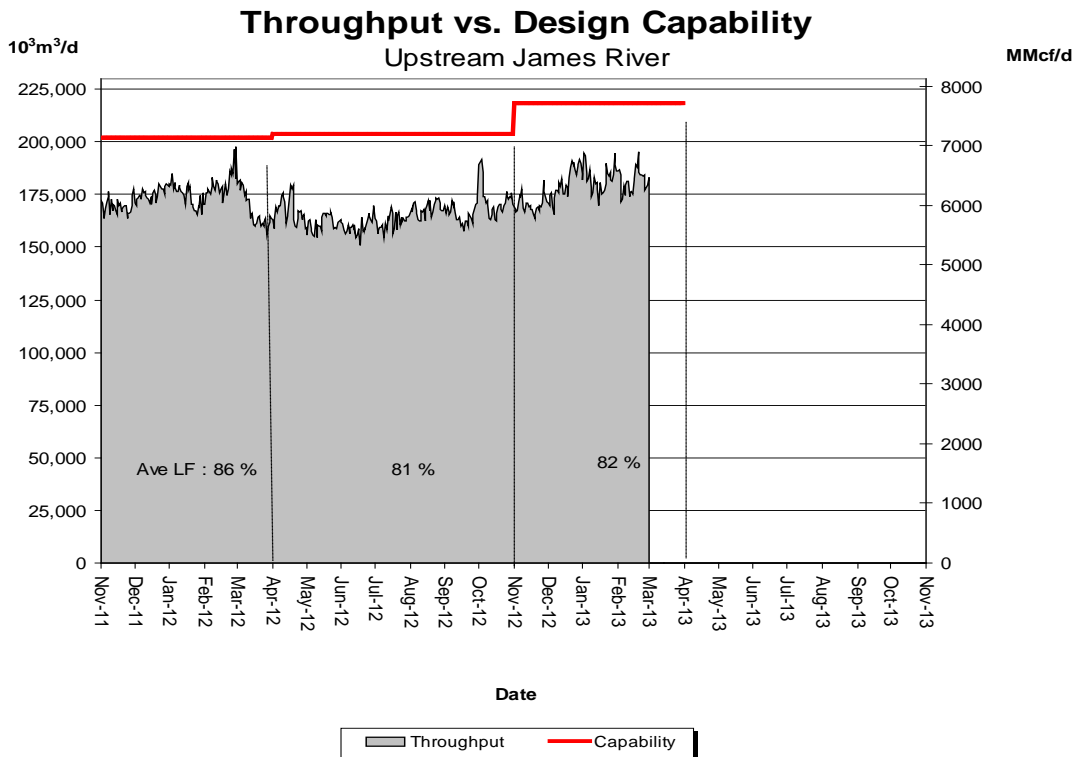


% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	81	84	78	82	83	82

DESIGN CAPABILITY UTILIZATION SOUTH and ALDERSON – FLOW WITHIN

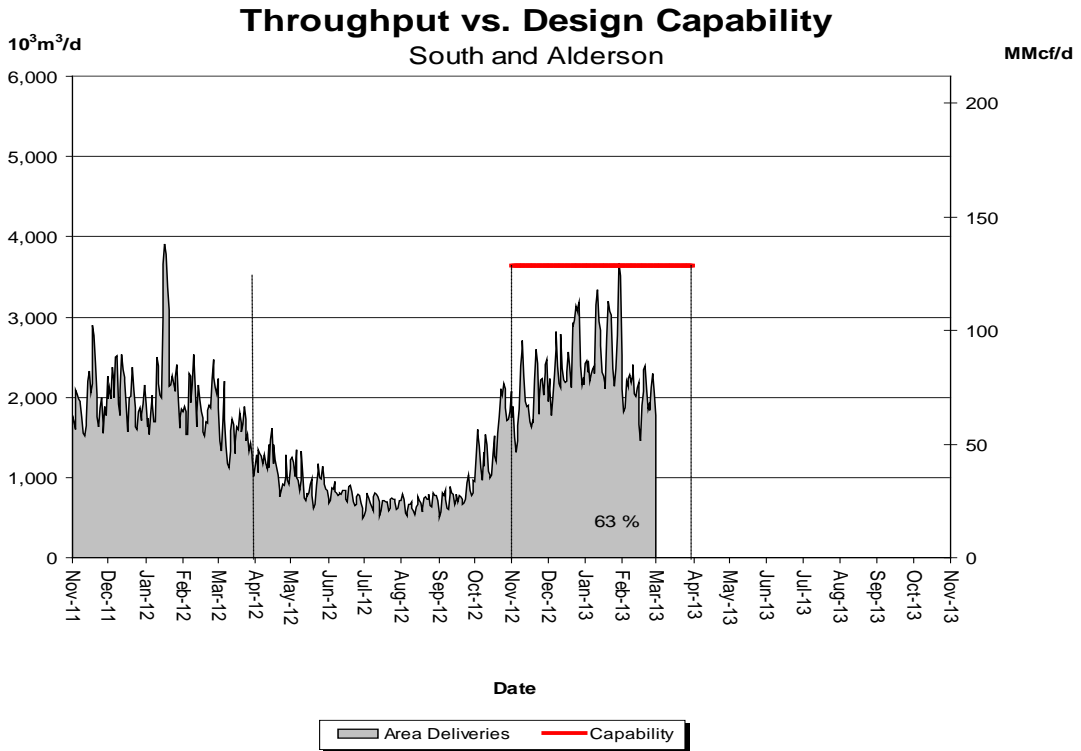


% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
			55	67	72	57

DESIGN CAPABILITY UTILIZATION RIMBEY-NEVIS – FLOW WITHIN





Throughput vs. Design Capability

Rimbey Nevis - Delivery Capability

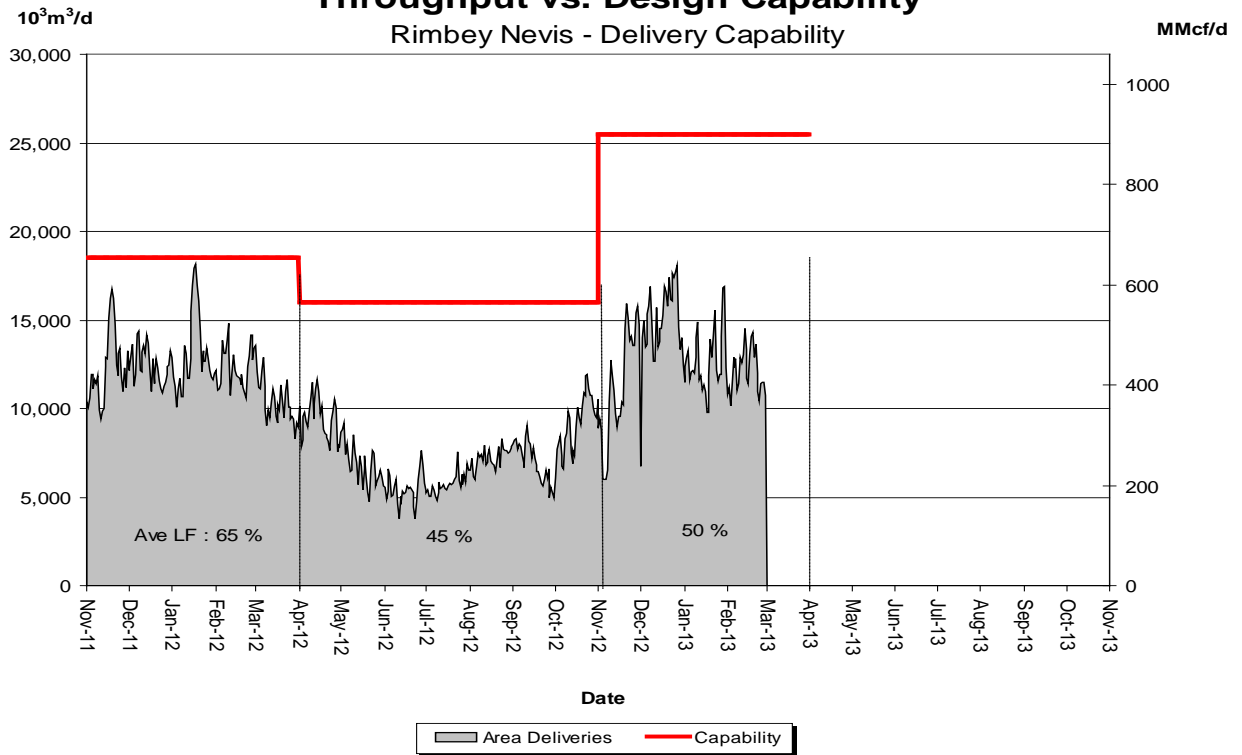



% Design Capability Utilization Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	43	58	44	58	50	48

DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE (James River to Princess)

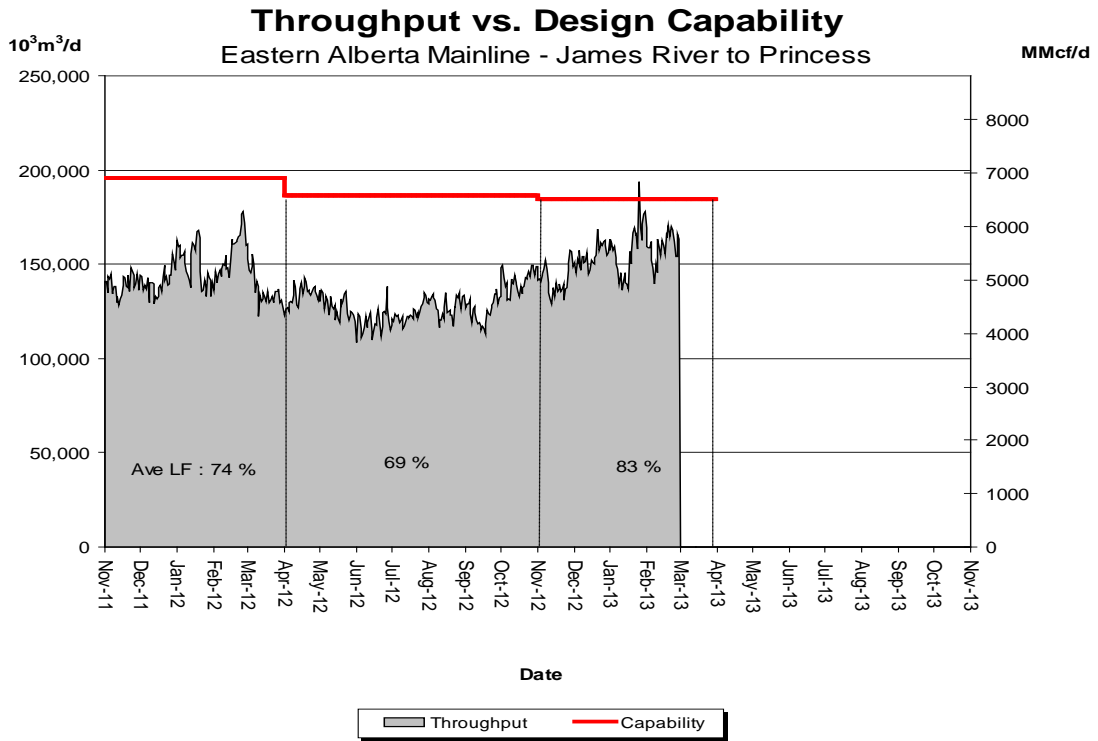



% Design Capability Utilization Monthly Average Actual Flow as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	67	76	76	84	85	86

DESIGN CAPABILITY UTILIZATION MEDICINE HAT – FLOW WITHIN

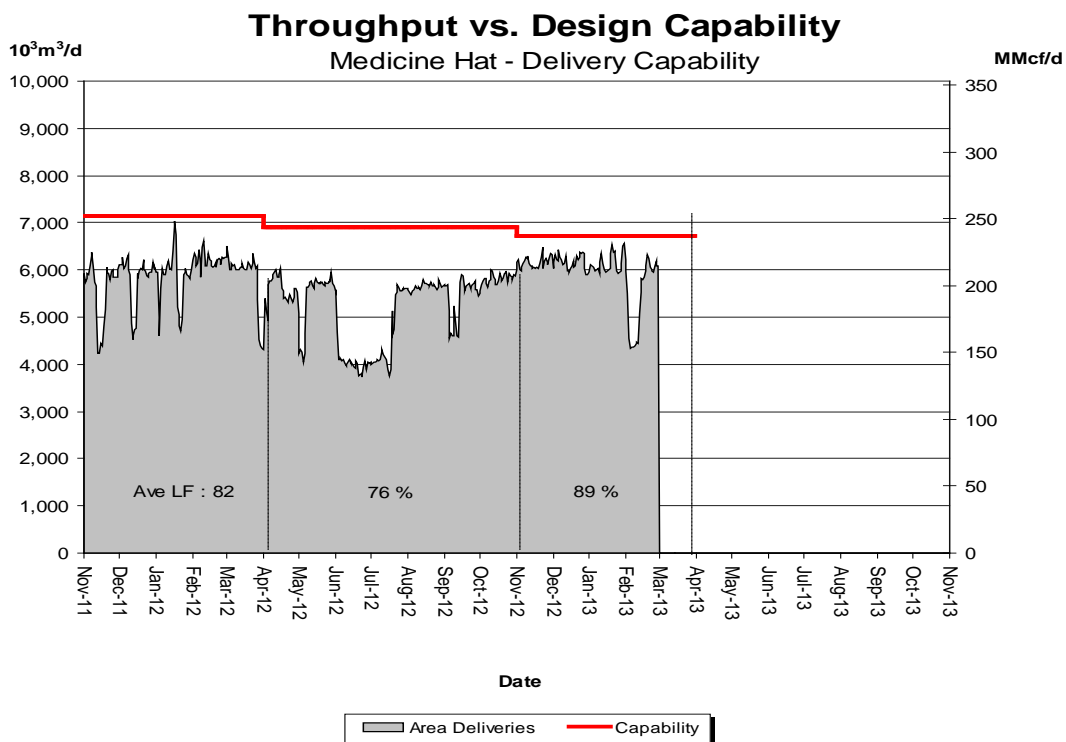



% Design Capability Utilization						
Monthly Average Area Deliveries as a Percentage of Design Capability						
Average Flow/ Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	78	84	91	91	91	81

DESIGN CAPABILITY UTILIZATION EASTERN ALBERTA MAINLINE (Princess to Empress / McNeill)

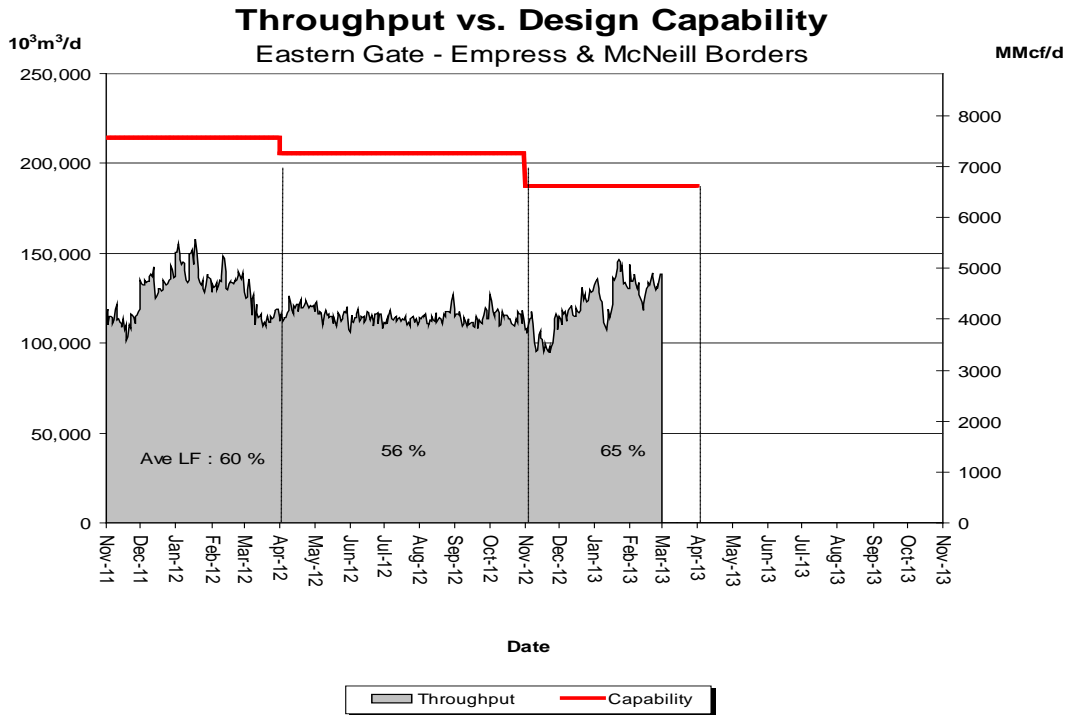

% Design Capability Utilization Average Actual Flow as a Percentage of Design Capability						
Average Flow / Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	55	56	56	64	69	71

DESIGN CAPABILITY UTILIZATION WESTERN ALBERTA MAINLINE (Alberta/B.C. and Alberta/Montana Borders)

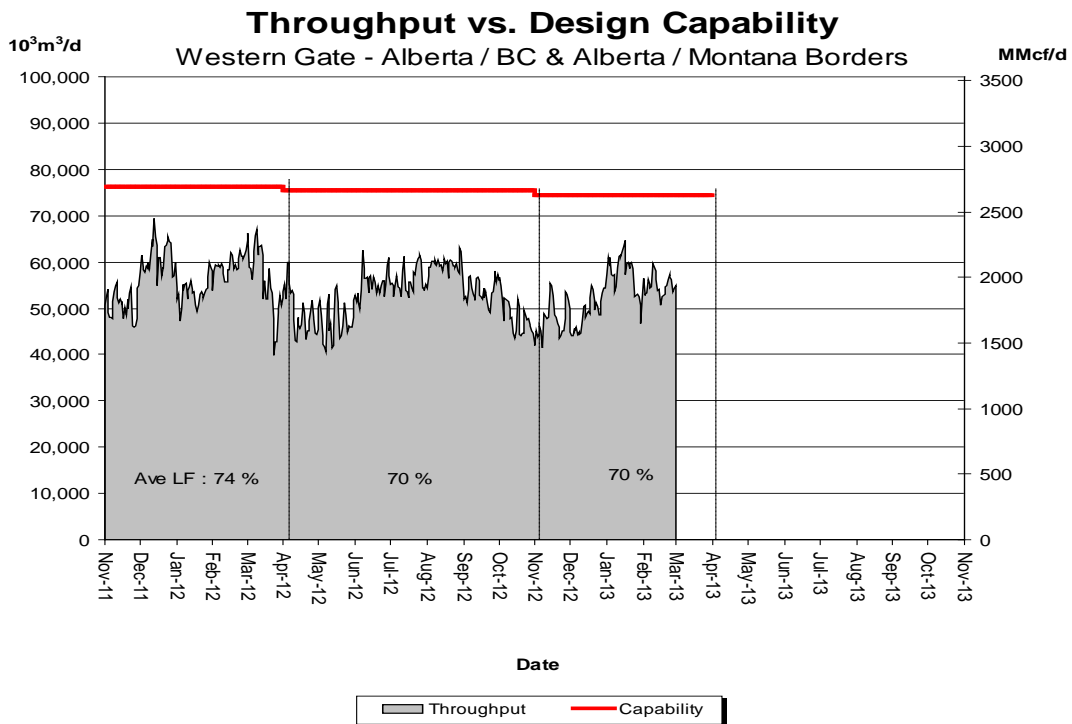

% Design Capability Utilization Average Actual Flow as a Percentage of Design Capability						
Average Flow / Design Capability	Sep	Oct	Nov	Dec	Jan	Feb
	71	64	64	66	77	74

HISTORICAL TRANSPORTATION SERVICE AVAILABILITY

December 1, 2012 to February 28, 2013 (3 Month Average)

Receipt Area	Segment	IT-R Service	Firm Service	Firm Service	% CD		Causes/Comments ⁽³⁾
		Available	Available	Restriction	Restricted ⁽¹⁾		
		(% of time)	(% of time)	(% of time)	Max	Average	
Peace River	UPRM 1	100	100	0	0	0	
	PRLL 2	100	100	0	0	0	
	NWML 3	100	100	0	0	0	
	GRDL 4	100	100	0	0	0	
	WAEX 5	100	100	0	0	0	
	JUDY 24	100	100	0	0	0	
	WRSY 26	100	100	0	0	0	
	LPRM 27	100	100	0	0	0	
	GPML 7	100	100	0	0	0	
Central	CENT 8	100	100	0	0	0	
	LPOL 9	100	100	0	0	0	
North & East Upstream of Bens Lake	LIEG 10	100	100	0	0	0	
	KIRB 11	100	100	0	0	0	
	MRTN 6	100	100	0	0	0	
	SMHI 12	100	100	0	0	0	
	REDL 13	100	100	0	0	0	
	COLD 14	100	100	0	0	0	
Downstream of Bens Lake	NLAT 15	100	100	0	0	0	
	ELAT 16	100	100	0	0	0	
	WAIN 23	100	100	0	0	0	
Rimbey/Nevis	ALEG 17	100	100	0	0	0	
Eastern Mainline	BLEG 18	100	100	0	0	0	
	EGAT 19	100	100	0	0	0	
	MLAT 20	100	100	0	0	0	
	SLAT 22	100	100	0	0	0	
Western Mainline	WGAT 21	100	100	0	0	0	

Borders	Available ⁽²⁾ (% of time)	IT-D Service	Firm Service	Firm Service	% CD Restricted ⁽¹⁾		Causes/Comments ⁽³⁾
		Available ⁽²⁾	Available	Restriction	Restricted ⁽¹⁾		
		(% of time)	(% of time)	(% of time)	Max	Average	
Empress/McNeill		100	100	0	0	0	
Alberta-BC		100	100	0	0	0	
Gordondale		100	100	0	0	0	

FUTURE FIRM TRANSPORTATION SERVICE AVAILABILITY (MAINLINE RESTRICTIONS)

Receipt and Delivery Firm Transportation Guidelines

Firm Transportation Location	Authorize Firm Transportation Service By	To Ensure Firm Transportation Service By
Summer construction (generally south of Edmonton)	November 2012	November 2014
Winter construction (generally north of Edmonton)	November 2012	April 2015

Estimated Firm Transportation Service Availability

Please refer to the following web site for
current FT-R / FT-D Availability Maps:

<http://staging.transcanada.com/customer-express/2801.html>

➤ If your needs for firm transportation service arise after the above dates to “Authorize Firm Transportation Service By”, NGTL will evaluate your new receipt firm transportation service or firm service transfer requests on a date-stamped basis.

Please consult with your Customer Sales Representative to discuss your Firm Transportation Service needs.

HOW TO USE THIS REPORT

Overview

This report contains recent historical information on the level of utilization of firm transportation Service Agreements on the NGTL system, relative usage of interruptible service, level of utilization of design pipeline capacity, and the availability of transportation services as an indication of system reliability.

Data is reported either by *Pipeline Segment* (26 on the system) or *Design Area* (13 on the system). Maps of both are included in the reference section.

Firm Transportation Service Contract Utilization

The Firm Transportation Service Contract Utilization report shows the percent utilization for each of the 26 NGTL pipeline segments and 3 major export delivery points comprising the total system. The utilization data is based on billed monthly volumes. Percent utilization is calculated as firm transportation service and firm transportation service + interruptible service divided by applicable receipt or delivery contract level. Historical Data involving billed volumes lags the current date by approximately two months.

Design Capability Utilization

The load factor/segment flow graphs show actual flow versus design capability values for various NGTL system areas. The graphs also show seasonal (winter/summer) design capability and average load factors for each season. Data used in these reports lags the current date by one month.

Design Flow Capability utilization is a function of several factors that include:

- Total market demand for Alberta natural gas.
- Seasonal changes in market demand for Alberta natural gas.
- Receipt nominating practices of customers individually and in aggregate to meet that level of demand.
- Effect of scheduled maintenance on actual flow requirement in a design area at any given time.
- Design assumptions used in determining required segment flow requirement.

HOW TO USE THIS REPORT - continued

Historical Transportation Service Availability

Transportation Service Availability is a system utilization measure that identifies the degree to which firm and interruptible transportation services are available on the NGTL system. It includes the historical frequency of service restriction experienced by the gas transmission network by service type and by pipeline segment.

The data shows the percentage of a given time period that a service type was available for a given section of the system. Service availability less than 100 percent means that some level of transportation service has been restricted for a portion of the time period.

Priority of transportation service on the NGTL system is firm transportation service, and then interruptible (IT). If transportation is restricted within a segment, all service within that segment of a lower priority will be affected.


Service availability is affected by a number of factors including scheduled and unscheduled maintenance, construction or other outages.

As a monthly feature the Historical Transportation Service Availability is shown as a three-month rolling average of transportation availability.

Future Firm Transportation Service Availability


The Future Firm Transportation Service Availability report presents guidelines and timing for all future firm transportation service requests.

NGTL Design Areas

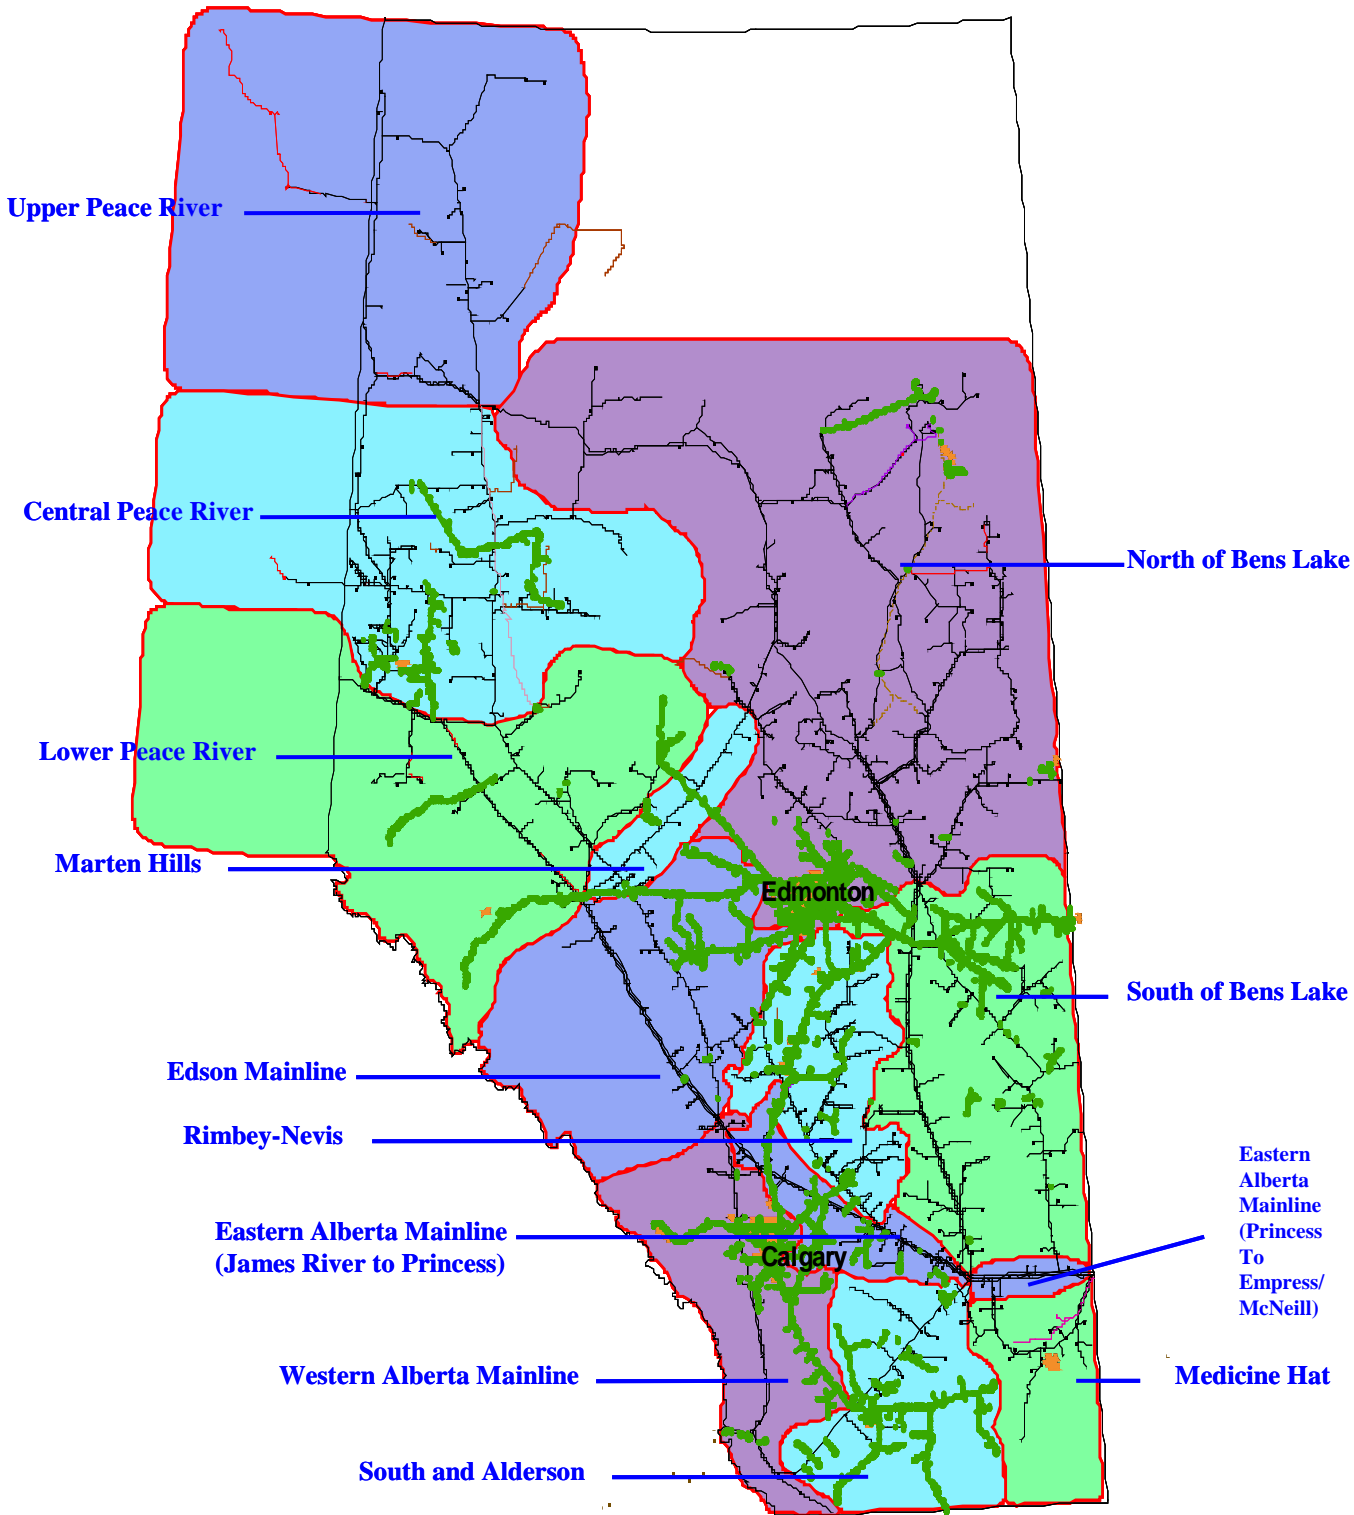

(Last updated Nov 2011)

NGTL Pipeline Segments

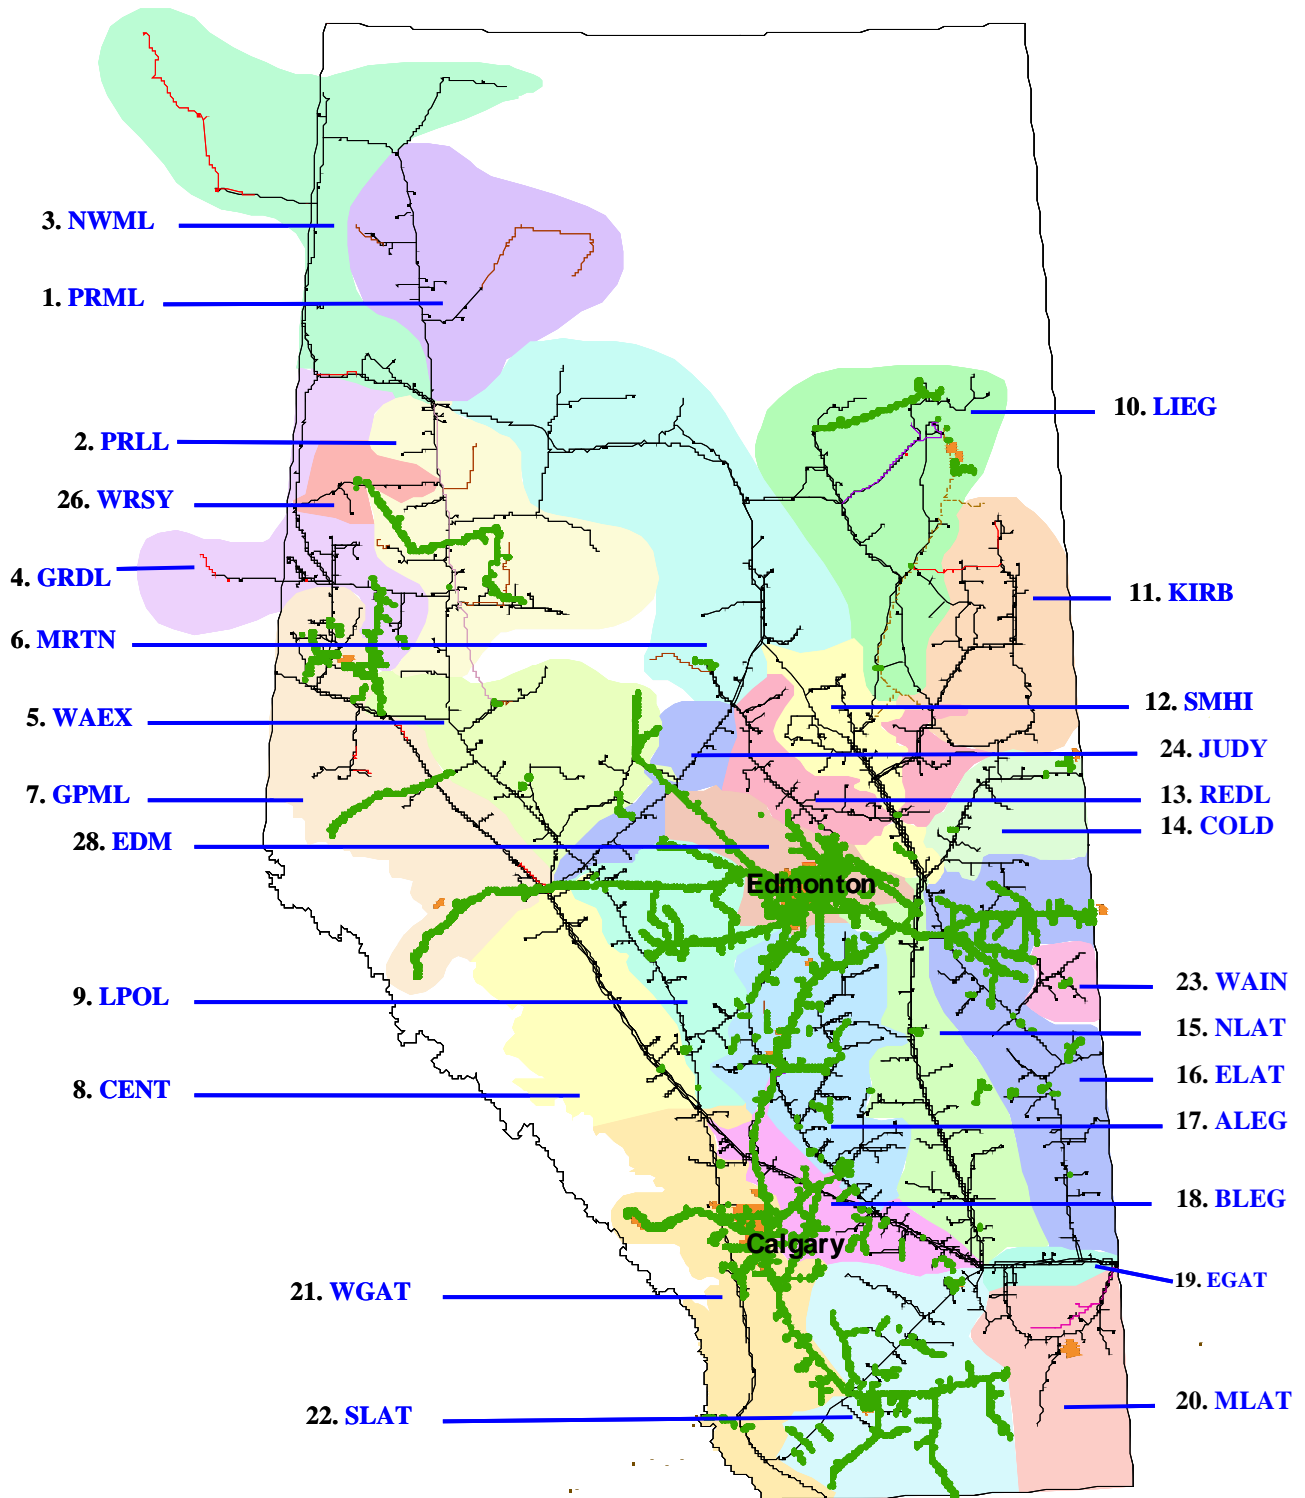

(Last updated Nov 2011)

DEFINITION OF TERMS

Design Capability Utilization

Actual Flow

The amount of gas flowing within or out of our design area.

Design Capability

The volume of gas that can be transported at various points on the pipeline system considering design assumptions.

AVGLF (Average Load Factor)

The ratio between average *Actual Flow* and *Design Capability*. It is calculated for every design season (summer/winter) as shown on the graphs.

Intra-Alberta Deliveries

The amount of sales gas flowing off the system within an area.

Receipt Flow

Aggregate of actual receipts within an area and the *Actual Flow* of the upstream area.

Historical Transportation Service Availability

Average % CD Restricted

The average percentage of the entire segment receipt contract demand restricted during periods of restriction.

Firm Service Available

The percentage of time that all requested firm transportation service requests were transported within a segment.

Firm Service Restriction

Percentage of time firm service is restricted.

IT-2 Service Available

The percentage of time that IT-2 service requests were transported.

Max % CD Restricted

The maximum percentage to which the entire segment contract demand was restricted.

Other

System Load Factor

The volume weighted average of the *Average Load Factor (AVGLF)* of all design areas on the system
